

**Upper Mississippi River Restoration Program Coordinating Committee  
Quarterly Meeting**

**November 16, 2022**

**Highlights and Action Items**

**Program Management**

- UMRR achieved an execution rate of 98.4 percent, obligating \$32.927 million of its \$33.17 million FY 22 funds. UMRR averaged a 97.7 percent execution rate from 2017 to 2022. Regional science and monitoring obligations reflect pre-funding of the FY 23 scope of work to ensure continuity of funding across fiscal years.
- On September 30, 2022, Congress passed a continuing resolution authority (CRA) extending current funding levels of the federal government until December 16, 2022. The President's FY 23 budget as well as the House and Senate FY 23 energy and water appropriations bills include \$55 million for UMRR. UMRR is proceeding with executing the Program at the \$55 million level. The final FY 23 appropriation is not yet known.
- The FY 23 draft plan of work for UMRR at a \$55 million funding scenario is as follows:
  - Regional Administration and Program Efforts – \$1,550,000
    - Regional management – \$1,280,000
    - Program database – \$100,000
    - Program Support Contract – \$120,000
    - Public Outreach – \$50,000
  - Regional Science and Monitoring – \$15,450,000
    - Long term resource monitoring – \$5,500,000
    - Regional science in support of restoration – \$8,350,000
    - Regional science staff support – \$200,000
    - Habitat evaluation (split across three districts) – \$1,275,000
    - Report to Congress – \$125,000
  - Habitat Restoration – \$38,000,000
    - Rock Island District – \$11,148,000
    - St. Louis District – \$13,502,000
    - St. Paul District – \$13,250,000
    - Model certification – \$100,000

**At a \$55 million funding level, regional science in support of restoration would increase from approximately \$3.8 million to \$8.3 million and habitat restoration funding in each district would increase from between \$6 million and \$7 million to between \$11 million and \$13 million.**

- The Senate WRDA 2022 draft language includes an annual appropriation authorization increase for the HREP element of UMRR from \$40 million to \$75 million. With LTRM's authorized

**appropriation level of \$15 million annually, the total UMRR annual authorized funding level would be \$90 million.**

- Updates to the UMRR 10-year implementation plan include adding Robinson Lake HREP to MVP, and extending schedules for Green Island, Harlow, and Oakwood Bottoms. **Twelve projects are anticipated to be in feasibility in FY 23, requiring considerable staff time from implementing partners. Increased appropriations would result in accelerated project schedules and expedited need for another project selection process. The next HREP selection process is anticipated to begin in calendar year 2024.** A UMRR and NESP program-neutral selection process was completed in 2009 and may be considered again to make efforts most efficient and complimentary.
- The second in-progress review of the 2022 UMRR Report to Congress with USACE Headquarters was held on August 29, 2022. MVD and USACE HQ then completed an initial review of the draft 2022 UMRR Report to Congress resulting in mostly editorial comments to improve clarity. **The revised report was routed to MVD and USACE HQ on November 9, 2022 for final approval. Marshall Plumley will distribute the finalized report to UMRR Coordinating Committee members in the coming weeks. The delivery of the report to Congress is anticipated in December 2022. A four-page handout will be developed to summarize the report. A small group will be convened to help develop key messages and talking points for the report to help partners communicate about the report release in spring 2023.**
- USACE will continue to fully integrate environmental justice into all aspects of its programs, including planning, design, construction, and operations and management. **Additional USACE guidance on environmental justice is anticipated in late November 2022. Following UMRR CC discussion at the August meeting and at the request of the UMRR Regional Program Manager, UMRBA staff sent an email to the UMRR Coordinating Committee on October 6, 2022 to designate staff from their respective agencies to participate in an *ad hoc* group to consider UMRR's roles in environmental justice.** The *ad hoc* group's first steps will include sharing their respective agencies' perspectives on approaches and best practices, methods, and tools related to environmental justice in their work and discussing how UMRR currently approaches environmental justice through habitat rehabilitation and enhancement projects. **A request for availability for the first discussion is anticipated to be sent in the coming weeks after all agencies have identified participants.**
- On August 31, 2022, the Coordinating Committee met to discuss revisions to the draft implementation issue papers. **On September 21, 2022, UMRBA staff sent an email asking Coordinating Committee members to identify supported and preferred actions to address each issue. On November 10, 2022, UMRBA staff distributed finalized implementation issue papers to the UMRR Coordinating Committee with draft recommendations removed. In the coming months, the Coordinating Committee will convene a meeting to establish broad consensus on the recommended suite of alternatives to address implementation issues and consider lead agency and personnel for each action to be pursued.**
- **A draft of the UMRR 2015-2025 Strategic Plan review report is nearly complete.** The report identifies what the program has done well and priority actions to fulfill the strategic plan. **A finalized report is anticipated to be submitted to UMRR Coordinating Committee members in the coming weeks. A meeting will be convened to review and discuss the results.** This meeting will likely be held on conjunction with the meeting to discuss the implementation issues papers.

### **Status and Trends**

- UMRBA staff are coordinating the development of a series of five two-page flyers related to findings presented in the 2022 UMRR LTRM status and trends report and are creating a plan for disseminating

flyers to the UMRR partnership and media outlets. Topics include fisheries, water quality and nutrients, floodplain forest loss, aquatic vegetation, and sedimentation. A finalized version of the fisheries flyer was presented to the UMRR Coordinating Committee in the meeting agenda packet and drafts of the sedimentation and floodplain forest loss flyers are in development. During various stages of development, flyers are reviewed by the report authors, UMRR Communications and Outreach Team, and A-Team members. Final draft versions are presented to the UMRR Coordinating Committee.

## **Communications**

- Using insights gained from the 2022 UMRR LTRM status and trends report release, the UMRR Communications and Outreach Team (COT) developed a set of best practices and drafted a six-month schedule template for similar future efforts. Recommendations include identifying key partners involved and their respective needs early in the process as well as intended communication methods and modes of dissemination to various stakeholder groups. When possible, messages should be tailored to specific geographic areas and anticipated FAQs should be developed prior to a press release.
- Future COT activities include developing communications materials to support publication of the 2022 UMRR Report to Congress, updating the UMRR communications and outreach plan, completing the UMRR video series, creating a communications inventory, and cooperating with advanced communications planning efforts around the 100<sup>th</sup> Anniversary of the Upper Mississippi River National Wildlife and Fish Refuge in 2024.

## **UMRR Showcase Presentations**

- Jennie Sauer presented LTRM accomplishments in FY 22, as follows:

### Partnership

- Collaboration with agencies on newly planned ecological assessment programs on the Columbia and Hudson River systems
- Collaboration with UMRR HREPs, including the Big Lake, Pool 4, and Lower Pool 13
- Successful completion of the UMRR 2022 virtual science meeting with over 100 participants representing 17 different agencies and organizations
- Contributions to future generations of scientists, including the water quality lab hosting 60 interns over the last 30 years and multiple graduate student research projects utilizing LTRM fish data.
- Completion of monitoring of the Illinois Waterway consolidated closure
- LTRM implementation planning efforts

### Publications

- Multiple publications based on 29 years of LTRM monitoring of fisheries and water quality and 24 years of aquatic vegetation monitoring, including the 2022 UMRR LTRM status and trends report and subsequent media coverage
- Advancing the UMRS resilience assessment including a new publication using the resist-accept-direct framework
- Development of a manuscript regarding side channel classification based on fish associations with physical metrics currently in review

### New Methods, Tools, and Procedures

- Successful upgrade of ScanLog/data transfer to sFTP
- Ongoing renovation of the LTRM water quality lab and temporary move to University of Wisconsin-La Crosse
- Creation of methods for high-accuracy mapping of emergent vegetation (wild rice) using UAS assets
- Land cover/use (LCU) 2020 mapping
- Mapping potential sensitivity to hydrogeomorphic change in the UMRS riverscape and development of supporting GIS database and query tool
- Refining the framework of Upper Mississippi River's ecosystem states based on predictions of plant distribution (and why) on the landscape and areas with high restoration potential
- Systematic analysis of hydrogeomorphic influences on native freshwater mussels including establishing population estimates in Pools 8 and 13
- Modeling projected patterns of forest recruitment and succession with and without inhibition of forest regeneration in areas currently occupied by invasive reed canary grass under different hydrologic scenarios

### Continuation of Important Work

- Ongoing work related to vital rates, genetics, and microchemistry of UMRS fishes
- Ongoing efforts to improve understanding of historic, contemporary, and future UMRS hydrology including development of a database template for historic and contemporary daily water service elevations at UMRS USACE gages.
- **Marshall Plumley presented Jennie Sauer with the Commanders Award for Public Service to recognize her exceptional service to UMRR and LTRM over 30 years.**
- District HREP managers presented on HREP accomplishments in FY 22, as follows:
  - MVP's FY 22 accomplishments include three ribbon cuttings to celebrate completion of Bass Ponds, Harpers Slough, and Conway Lake HREPs. Two accomplishments outside of UMRR include beneficially using dredged material at Pigs Eye Lake, a CAP 204 project, to create six islands and selection of Upper Pool 4 Islands as a CAP 1122 pilot project. The project will add islands to upper Lake Pepin. MVP public affairs created five videos and multiple social media posts featuring HREPs and participated in the UMRR Earth Day campaign.
  - MVR's FY 22 accomplishments include advancing feasibility studies on four HREPs, awarding a construction contract for Steamboat Island, and completing construction of Keithsburg Stage I and Stage IIA as well as various components of the Beaver Island HREP. The district developed a ribbon cutting video to celebrate completion of the Pool 12 Overwintering HREP. Aquatic vegetation plantings at Huron Island have been successful and blanket purchase agreements have advanced tree planting and clearing as well as timber inventory efforts in the District. MVR public affairs created three videos and featured multiple social media posts on UMRR and LTRM activities.
  - MVS's FY 22 accomplishments include advancing construction on three HREPs, design on two HREPs, and feasibility on two HREPs. The sediment deflection berm was completed at Crains Island, UMRR's first open river project, and pump stations are nearly complete at Clarence Cannon HREP. The District has drafted three new fact sheets and toured Cypress Creek Refuge

to discuss restoration opportunities with the USFWS Refuge Manager. Site visits to Swan Lake, Cuivre Island, Calhoun Point, and Dresser Island helped identify construction and operation lessons learned. The Swan Lake Flood Damage Assessment letter report was advanced.

### **Long Term Resource Monitoring and Science**

- Accomplishments of the fourth quarter of FY 22 include publication of the following manuscripts and reports:
  - *Annual Summer Submersed Macrophyte Standing Stocks Estimated From Long-Term Monitoring Data in the Upper Mississippi River*
  - *Trophic reorganization of native planktivorous fishes at different density extremes of bigheaded carps in the Illinois and Mississippi Rivers, USA.*
  - *Recommendations report regarding water level management to achieve ecological goals in the Upper Mississippi River System*
- Renovation of the LTRM water quality laboratory, which has temporarily moved to the University of Wisconsin-La Crosse, is ongoing. The laboratory renovation is expected to be completed in July 2023.
- **UMRR is operating under a \$55 million funding scenario for FY 23, in which LTRM is allocated \$13.85 million. Allocations compared to the FY 22 funding level are as follows:**
  - Base monitoring increases to \$5.5 million from \$5 million
  - Science in support restoration (analysis under base) increases to \$1.5 million from \$1.3 million
  - Science in support of restoration and management increases to \$6.85 million from \$2.5 million

**The LTRM FY 23 \$7.4 million base monitoring and analysis-under-base program covers field stations, UMESC, and Corps technical and science representatives. Under the continuing resolution funding restrictions, LTRM is funded to continue base monitoring until more appropriations are received. High priority funding items for science in support of restoration total \$1.975 million and include:**

- LTRM balance: \$464,671
- Ecohydrology: \$459,797
- LC processing (last year): \$335,238
- Proposal adjustments: \$28,884
- Macroinvertebrate contaminants: \$77,483
- Herbarium: \$21,000
- Future landscape modeling: \$588,674

**Remaining funds of approximately \$4.9 million may be used to purchase equipment for field stations and the water quality lab, fund the final year of LCU processing, advance additional FY 22 science proposals, and/or update topobathy. The latter would include financial support from NESP.**

- The *ad hoc* LTRM implementation planning team has been tasked with determining research opportunities to expand the understanding of UMRS restoration and management. In part, an objective for this effort is to identify and prioritize research needs under increased potential for additional funding following the authorized increase in WRDA 2022.

Over the past several months, the implementation planning team has drafted objective statements and identified and prioritized information needs in four broad categories: floodplain ecology, hydrogeomorphic change, aquatic ecology, and restoration applications. Possible actions to address information needs include employing short-term research studies, adding capacity for analyzing existing LTRM data, spatially expanding baseline monitoring, and adding new long term monitoring components. **The team held an in-person workshop on September 13-15, 2022 to finalize scoring criteria and information needs. Agencies submitted final scores of information needs on November 10, 2022.** The implementation planning team is scheduled to meet on November 17, 2022 to review scoring results. A small subgroup will develop approximate cost estimates associated with necessary actions to address each information need. The implementation planning team will then discuss how to optimize actions based on scores and estimated costs.

- The A-Team met on October 25, 2022. The agenda covered the following items:
  - Updating the A-Team Corner and the Corps webpages regarding LTRM information
  - Management implications of a resilience assessment of the UMRS, including application of the resist-accept-direct framework
  - The status of aquatic vegetation in Pool 13
  - Potential A-Team roles in HREP/LTRM integration
  - Two-page flyers communicating the major findings from the 2022 UMRR LTRM status and trends report
  - Wisconsin field station staff

As next steps, the A-Team will request that field station staff review information on the A-Team Corner and Corps webpages and submit updated information.

### **Habitat Restoration**

- MVP's planning priorities include Robinson Lake, Big Lake - Pool 4, and Reno Bottoms. A kick-off meeting for Robinson Lake is being planned and will use the same PDT as the Big Lake Pool 4 project. The Reno Bottoms draft report was completed and released for public review. A design contract award for Lower Pool 10 is expected at the end of this month. Construction was completed at Harpers Slough, Bass Ponds, and Conway Lake HREPs. O&M manuals are nearly complete. A contract to complete McGregor Lake HREP construction was awarded at the end of the last fiscal year. Other efforts in the District include development of a Trempealeau HREP letter report outlining repair needs and the development of storymaps for new HREPs.
- MVR's planning priorities include Lower Pool 13, Green Island, Pool 12 Forestry, and Quincy Bay. The District's design priority is Steamboat Island Stage II. MVR has six projects in construction including Pool 12 Overwintering, Beaver Island Stage IB, Steamboat Island Stage I, Keithsburg Division Stages I and II, and Huron Island Stage III. The District is working to turn over the Pool 12 Overwintering Stage II project to the sponsor. A construction contract for Steamboat Island Stage I was awarded on August 31, 2022. A ribbon cutting for Huron Island Stage II was held on September 7, 2022. MVR is working to address sponsor comments on the Upper Pool 13 fact sheet.
- MVS's planning priorities include West Alton Islands and Yorkinut Slough. MVS's design priorities include Piasa & Eagles Nest, Harlow Island, Oakwood Bottoms, and Crains Island. MVS has three projects in construction: Crains Island, Piasa and Eagles Nest, and Clarence Cannon Refuge HREPs. A construction contract award for Stage II of Piasa and Eagles Nest is anticipated for the second quarter of FY 23.

## **LTRM and HREP Special Reports**

- Mike Spear, INHS, presented on fish community response to decreased vessel traffic on the Illinois Waterway. Consolidated extended closure of eight locks and dams in 2020 spurred a multi-agency monitoring effort from 2019 to 2021 to assess changes in river conditions from decreased navigation traffic. This was a unique ecosystem-scale opportunity to assess anthropogenic impacts of vessel traffic to a large river using a before/after/control impact study design. Three variables were evaluated including vessel traffic intensity, water quality, and fish communities in the main channel for direct impacts, side channels without direct traffic, and backwaters separated from noise and turbidity. Navigation pools showed a 50 percent to 100 percent decrease in vessel traffic during the closure year of 2020. In addition, catch of sound-sensitive and rheophilic fish taxa as well as Gizzard shad increased in main and side channel habitats as compared to the backwater “quasi-control” condition.
- Collin Moratz, USACE, presented an update on aquatic vegetation plantings at the Huron Island HREP. ERDC provided support from FY 18 to FY 20 to establish native aquatic vegetation at the project site. ERDC used flood tolerant native plant species of regional provenance and monitored plantings for adaptive management purposes. Herbivory exclosures were installed and initial specimens planted in August 2019. Assessments in 2020 indicated some mortality due to 2019 flooding, but also that some species had established outside exclosures. An assessment June 2021 showed unprotected arrowhead recruitment, additional spread of longleaf pondweed from exclosures, and good to high survival of ten species in exclosures. An additional planting was conducted in July 2021. An assessment in September 2021 showed high survival of 13 species in exclosures and rushes and arrowheads observed in unprotected areas. From July 26-28, 2022 a three day field campaign was conducted with ERDC, MVR, and Iowa DNR to establish larger exclosures with additional plantings. During an assessment on September 21, 2022, pens showed 70 percent to 99 percent coverage with some plants spreading from exclosures showing signs of herbivore damage. Overall, there was limited spread observed for both emergents and SAV beyond protected exclosures, likely due to herbivory pressure both aquatic and from terrestrial herbivores. One remaining question is whether a critical mass can be reached, whereby unprotected plant communities are robust to herbivory.

## **Other Business**

Upcoming quarterly meetings are as follows:

- **February/March 2023 – Virtual**
  - UMRBA quarterly meeting – February 28
  - **UMRR Coordinating Committee quarterly meeting – March 1**
- **May 2023 – St. Paul, MN**
  - UMRBA quarterly meeting – May 23
  - **UMRR Coordinating Committee quarterly meeting – May 24**
- **August 2023 – La Crosse, WI**
  - UMRBA quarterly meeting – August 8
  - **UMRR Coordinating Committee quarterly meeting – August 9**

**UMRR COORDINATING COMMITTEE -  
REGIONAL MANAGEMENT  
AND PARTNERSHIP  
COLLABORATION**



Marshall Plumley  
Regional Program Manager  
St. Paul District  
Rock Island District  
St. Louis District

16 November 2022

1

**REGIONAL MANAGEMENT AND PARTNERSHIP  
COLLABORATION**

- FY 2022 Fiscal Update and FY 23 Outlook
- 2022 Report to Congress
- Environmental Justice
- Implementation Issues
- Strategic and Operation Plan review



2

**FY 2022 FISCAL UPDATE AND  
FY 2023 OUTLOOK**



3

**FY 22 APPROPRIATIONS**

President's Budget	\$33,170,000
House	\$33,170,000
Senate	\$33,170,000
 FINAL APPROPRIATION	 \$33,170,000
Infrastructure Bill	\$0
FY 22 Workplan	\$0



4

**FINANCIAL REPORTING**

UMRR Quarterly Budget Report: St. Paul District  
FY2022 Q4, Report Date: Tue Oct 11 2022

Project Name							FY2022 Financials			
Non-Federal		Federal		Total	Carry In	Allocation	Funds Available	Actual Obligations		
Bear Ponds, Marsh, and Wetlands	\$6,300,000	\$6,300,000			\$277,600	\$277,600	\$606,899			
Conway Lake	\$741,900	\$741,900			\$200,000	\$200,000	<b>\$346,925</b>			
Harpers Slough	\$15,675,000	\$15,675,000			\$2,400,000	\$2,400,000	<b>\$27,959</b>			
Island and Island Complex	\$17,000,000	\$17,000,000			\$93,793	\$150,000	\$443,793	\$153,197		
Islandwood 4, Big Lake						\$10,000	\$10,000	\$428,241		
McGregor Lake	\$22,500,000	\$22,500,000			\$1,180,000	\$1,180,000	\$4,200,000			
None Existing	\$10,000,000	\$10,000,000			\$52,323	\$360,000	\$417,223	\$405,445		
<b>Total</b>	<b>\$77,938,000</b>	<b>\$77,938,000</b>			<b>\$146,116</b>	<b>\$6,718,000</b>	<b>\$6,864,116</b>	<b>\$5,419,753</b>		

**Habitat Rehabilitation**

Subcategory							FY2022 Financials			
Carry In		Allocation		Funds Available	Obligations					
District Program Management					\$623,927					
<b>Total</b>					<b>\$623,927</b>					

**Regional Program Administration**

Subcategory							FY2022 Financials			
Carry In		Allocation		Funds Available	Obligations					
Habitat Eval/Monitoring					\$275,858					
<b>Total</b>					<b>\$275,858</b>					

St. Paul Total				Carry In	Allocation	Funds Available	Actual Obligations
\$146,116				\$6,718,000	\$6,864,116	\$5,419,753	



5

**FINANCIAL REPORTING**

UMRR Quarterly Budget Report: Rock Island District  
FY2022 Q4, Report Date: Tue Oct 11 2022

**Habitat Projects**

Project Name							FY2022 Financials			
Non-Federal		Federal		Total	Carry In	Allocation	Funds Available	Actual		
Beaver Island	\$25,248,000	\$25,248,000			\$22,258,000		\$1,038,000	\$200,129		
Cottonwood Slough	\$1,000,000	\$1,000,000			\$1,000,000		\$1,000,000	\$1,000,000		
Harmon Island	\$17,735,000	\$17,735,000			\$15,773,000		\$1,962,000	\$92,189		
Macomb Slough	\$204,443,000	\$204,443,000					\$5,648,499	\$204,443,000		
Macomb Slough Division										
Lower Pool 13	\$25,290,000	\$25,290,000			\$1,027,000		\$200,000	\$244,707		
Lower Pool 1-2							\$500,000	\$500,000		
Lower Pool 2-3							\$500,000	\$10,037		
Lower Pool 3-4										
Lower Pool 4-5										
Lower Pool 5-6										
Lower Pool 6-7										
Lower Pool 7-8										
Lower Pool 8-9										
Lower Pool 9-10										
Lower Pool 10-11										
Lower Pool 11-12										
Lower Pool 12-13										
Lower Pool 13-14										
Lower Pool 14-15										
Lower Pool 15-16										
Lower Pool 16-17										
Lower Pool 17-18										
Lower Pool 18-19										
Lower Pool 19-20										
Lower Pool 20-21										
Lower Pool 21-22										
Lower Pool 22-23										
Lower Pool 23-24										
Lower Pool 24-25										
Lower Pool 25-26										
Lower Pool 26-27										
Lower Pool 27-28										
Lower Pool 28-29										
Lower Pool 29-30										
Lower Pool 30-31										
Lower Pool 31-32										
Lower Pool 32-33										
Lower Pool 33-34										
Lower Pool 34-35										
Lower Pool 35-36										
Lower Pool 36-37										
Lower Pool 37-38										
Lower Pool 38-39										
Lower Pool 39-40										
Lower Pool 40-41										
Lower Pool 41-42										
Lower Pool 42-43										
Lower Pool 43-44										
Lower Pool 44-45										
Lower Pool 45-46										
Lower Pool 46-47										
Lower Pool 47-48										
Lower Pool 48-49										
Lower Pool 49-50										
Lower Pool 50-51										
Lower Pool 51-52										
Lower Pool 52-53										
Lower Pool 53-54										
Lower Pool 54-55										
Lower Pool 55-56										
Lower Pool 56-57										
Lower Pool 57-58										
Lower Pool 58-59										
Lower Pool 59-60										
Lower Pool 60-61										
Lower Pool 61-62										
Lower Pool 62-63										
Lower Pool 63-64										
Lower Pool 64-65										
Lower Pool 65-66										
Lower Pool 66-67										
Lower Pool 67-68										
Lower Pool 68-69										
Lower Pool 69-70										
Lower Pool 70-71										
Lower Pool 71-72										
Lower Pool 72-73										
Lower Pool 73-74										
Lower Pool 74-75										
Lower Pool 75-76										
Lower Pool 76-77										
Lower Pool 77-78										
Lower Pool 78-79										
Lower Pool 79-80										
Lower Pool 80-81										
Lower Pool 81-82										
Lower Pool 82-83										
Lower Pool 83-84										
Lower Pool 84-85										
Lower Pool 85-86										
Lower Pool 86-87										
Lower Pool 87-88										
Lower Pool 88-89										
Lower Pool 89-90										
Lower Pool 90-91										
Lower Pool 91-92										
Lower Pool 92-93										
Lower Pool 93-94										
Lower Pool 94-95										
Lower Pool 95-96										
Lower Pool 96-97										
Lower Pool 97-98										
Lower Pool 98-99										
Lower Pool 99-100										
Lower Pool 100-101										
Lower Pool 101-102										
Lower Pool 102-103										
Lower Pool 103-104										
Lower Pool 104-105										
Lower Pool 105-106										
Lower Pool 106-107										
Lower Pool 107-108										
Lower Pool 108-109										
Lower Pool 109-110										
Lower Pool 110-111										
Lower Pool 111-112										
Lower Pool 112-113										
Lower Pool 113-114										
Lower Pool 114-115										
Lower Pool 115-116										
Lower Pool 116-117										
Lower Pool 117-118										
Lower Pool 118-119										
Lower Pool 119-120										
Lower Pool 120-121										
Lower Pool 121-122										
Lower Pool 122-123										
Lower Pool 123-124										
Lower Pool 124-125										
Lower Pool 125-126										
Lower Pool 126-127										
Lower Pool 127-128										
Lower Pool 128-129										
Lower Pool 129-130										
Lower Pool 130-131										
Lower Pool 131-132										
Lower Pool 132-133										
Lower Pool 133-134										
Lower Pool 134-135										
Lower Pool 135-136										
Lower Pool 136-137										
Lower Pool 137-138										
Lower Pool 138-139										
Lower Pool 139-140										
Lower Pool 140-141										
Lower Pool 141-142										
Lower Pool 142-143										
Lower Pool 143-144										
Lower Pool 144-145										
Lower Pool 145-146										
Lower Pool 146-147										
Lower Pool 147-148										
Lower Pool 148-149										
Lower Pool 149-150										
Lower Pool 150-151										
Lower Pool 151-152										
Lower Pool 152-153										
Lower Pool 153-154										
Lower Pool 154-155										

**7**

**FINANCIAL REPORTING**

UMRR Quarterly Budget Report: St. Louis District  
FY2022 Q4 Report Date: Tue Oct 11 2022

**Habitat Projects**

Project Name	Cost Estimates			FY2022 Financials			
	Non-Federal	Federal	Total	Carry In	Allocation	Funds Available	Actual Obligations
Clarence Island	\$29,800,000	\$29,800,000		\$28,498	\$1,900,000	\$1,928,498	\$244,967
Cranes Island	\$36,562,000	\$36,562,000		-	\$325,000	\$323,500	\$24,450
Harlow Island	\$37,971,000	\$37,971,000		-	-	-	-
Island Bottoms	\$29,000,000	\$29,000,000		-	\$67,850,000	\$1,098,386	-
Mississippi Islands	\$26,746,000	\$26,746,000		-	\$2,575,000	\$2,575,000	\$3,524,831
West Alton Islands	-	-	-	-	\$436,000	\$436,000	\$329,954
Waukegan Slough, IL	\$8,500,000	\$8,500,000		\$9,343	\$425,000	\$434,343	\$969,196
<b>Total</b>	<b>\$168,579,000</b>	<b>\$168,579,000</b>		<b>\$37,841</b>	<b>\$7,150,000</b>	<b>\$7,187,841</b>	<b>\$6,167,561</b>

**Habitat Rehabilitation**

Subcategory	FY2022 Financials			
	Carry In	Allocation	Funds Available	Obligations
District Program Management	-	-	-	\$709,457
<b>Total</b>	<b>-</b>	<b>-</b>	<b>-</b>	<b>\$709,457</b>

**Regional Program Administration**

Subcategory	FY2022 Financials			
	Carry In	Allocation	Funds Available	Obligations
Habitat Eval/Monitoring	-	-	-	\$390,481
<b>Total</b>	<b>-</b>	<b>-</b>	<b>-</b>	<b>\$390,481</b>

<b>St. Louis Total</b>	<b>\$37,841</b>	<b>\$7,150,000</b>	<b>\$7,187,841</b>	<b>\$7,267,499</b>
------------------------	-----------------	--------------------	--------------------	--------------------



**8**

**FY22 PLAN OF WORK**

	Budget	Obligations 4th Qtr
<b>TOTAL FY22 Program</b>	<b>\$33,583,764</b>	<b>\$32,927,400</b>
<b>Regional Administration and Program Efforts</b>	<b>\$ 1,450,000</b>	<b>\$ 1,115,245</b>
Regional Management	\$ 1,180,000	
Program Database	\$ 100,000	
Program Support Contract (UMRBA)	\$ 120,000	
Public Outreach	\$ 50,000	
<b>Regional Science and Monitoring</b>	<b>\$10,250,096</b>	<b>\$11,410,061</b>
LTRM (Base Monitoring)	\$ 5,000,000	
UMRR Regional Science In Support Rehabilitation/Mgmt. (MIPRs, Contracts, and Labor)	\$ 3,800,000	
UMRR Regional (Integration, Adapt. Mgmt.)	\$ 200,000	
Habitat Evaluation (split between MVS,MVR,MVP)	\$ 1,125,096	
Report to Congress	\$ 125,000	
<b>District Habitat Rehabilitation Efforts</b>	<b>\$21,883,668</b>	<b>\$20,402,094</b>
(Planning and Construction)		
St. Paul District	\$ 6,684,116	
Rock Island District	\$ 7,731,711	
St. Louis District	\$ 7,187,841	
Model Cent.	\$ 100,000	



7


8

**9**

**EXECUTION**

Fiscal Year	Total Obligated
2011- 2016 Average	97.0 percent
2017	92.0 percent
2018	99.1 percent
2019	99.1 percent
2020	98.5 percent
2021	98.8 percent
2022	98.5 percent
<b>2017 - 2022 Average</b>	<b>97.7 percent</b>



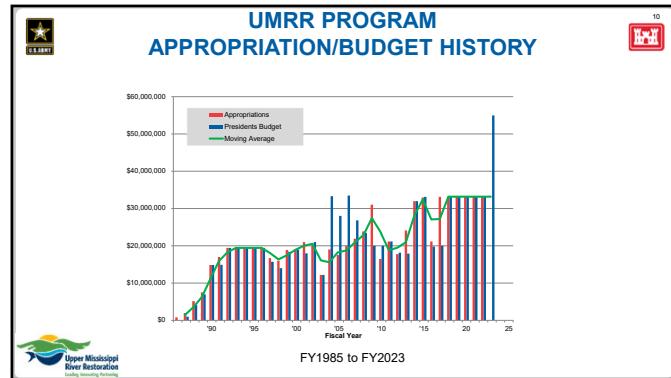

9

10

**11**

**FY 23 APPROPRIATIONS**

President's Budget	<b>\$55,000,000</b>
House	<b>\$55,000,000</b>
Senate	<b>\$55,000,000</b>
<b>FINAL APPROPRIATION</b>	<b>\$?</b>
<b>FY 23 Workplan</b>	<b>\$?</b>



**12**

**FY23 DRAFT PLAN OF WORK**

	Budget
<b>TOTAL FY22 Program</b>	<b>\$55,000,000</b>
<b>Regional Administration and Program Efforts</b>	<b>\$ 1,550,000</b>
Regional Management	\$ 1,280,000
Program Database	\$ 100,000
Program Support Contract (UMRBA)	\$ 120,000
Public Outreach	\$ 50,000
<b>Regional Science and Monitoring</b>	<b>\$15,450,000</b>
LTRM (Base Monitoring)	\$ 5,500,000
UMRR Regional Science In Support Rehabilitation/Mgmt. (MIPRs, Contracts, and Labor)	\$ 8,350,000
UMRR Regional (Integration, Adapt. Mgmt.)	\$ 200,000
Habitat Evaluation (split between MVS,MVR,MVP)	\$ 1,275,000
Report to Congress	\$ 125,000
<b>District Habitat Rehabilitation Efforts</b>	<b>\$38,000,000</b>
(Planning and Construction)	
St. Paul District	\$11,148,000
Rock Island District	\$13,510,000
St. Louis District	\$13,250,000
Model Cent.	\$ 100,000



11

12

## POTENTIAL WRDA 2022 CHANGES TO UMRR


*Senate* SEC. 317. UPPER MISSISSIPPI RIVER SYSTEM ENVIRONMENTAL MANAGEMENT PROGRAM.

Section 1103(e)(3) of the Water Resources Development Act of 1986 (33 U.S.C. 652(e)) is amended by striking "\$40,000,000" and inserting "\$75,000,000".

HREP \$75,000,000 + LTRM \$15,000,000

\$90,000,000

13

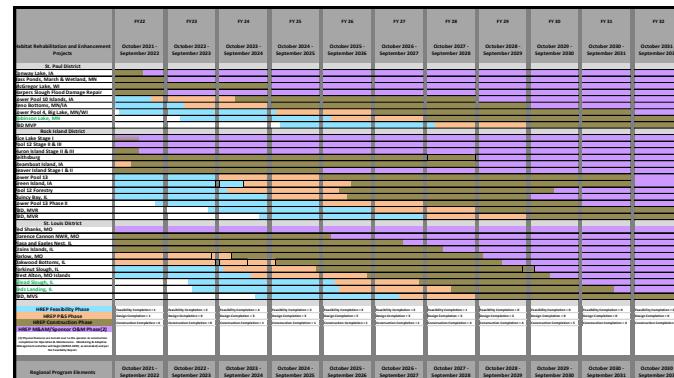


14

15


## 2022 REPORT TO CONGRESS

15

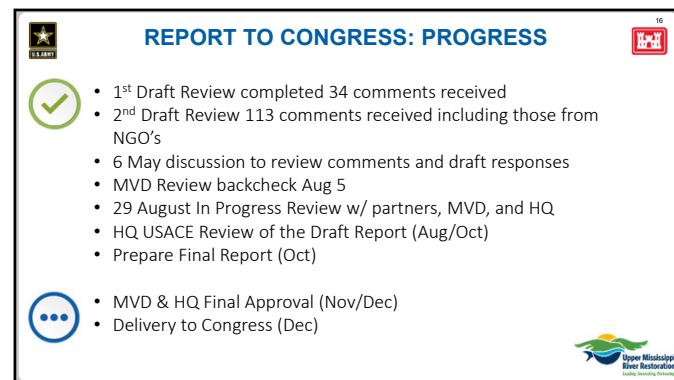

16

17

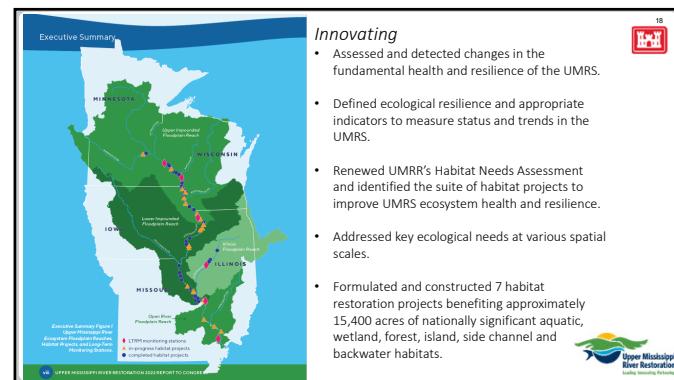

18

**19**

**Partnersing**

- Actively exchanged information with UMRS watershed, national, and international partners.
- Evaluated and learned from constructed habitat restoration projects.
- Applied adaptive management principles to address risk and uncertainty.
- Collaborated with partners to further inform issues related to project partnership agreements.

Upper Mississippi River Restoration  
Leading. Innovating. Partnering.

**20**

**Conclusions and Recommendations**

**Recommendations in the 2022 RTC:**

- Apply defined ecological resilience concepts.
- Apply the UMRR Habitat Needs Assessment II.
- Continue to identify and construct habitat projects that improve the Upper Mississippi River Systems ecosystem health and resilience.
- Evaluate and learn from constructed habitat projects to inform future restoration and management.
- Engage the partnership in 2024 in preparing the next UMRR Strategic Plan.

Upper Mississippi River Restoration  
Leading. Innovating. Partnering.

**21**

**Conclusions and Recommendations**

**Recommendations in the 2022 RTC:**

- Apply adaptive management principles to address risk and uncertainty.
- Assess, and detect changes in, the fundamental health and resilience of the Upper Mississippi River ecosystem by continuing to monitor and evaluate its key ecological components.
- Provide critical insights and understanding regarding a range of key ecological questions... in order to inform and improve management and restoration of the Upper Mississippi River ecosystem.

Upper Mississippi River Restoration  
Leading. Innovating. Partnering.

**22**

**Conclusions and Recommendations**

**Recommendations in the 2022 RTC:**

- Work with key organizations and individuals in the Upper Mississippi River watershed.
- Provide information to organizations and individuals whose actions and decisions affect the Upper Mississippi River ecosystem.
- Promote a common vision and sense of purpose, transparency, and accountability among UMRR's implementing partner agencies.
- Implement UMRR as outlined in Joint Charter.
- The Corps and non-federal sponsors should continue to work together to further inform issues related to execution of PPAs.

**23**

**UMRR 2022 Report to Congress**


**Letters of Support**

- U.S. Fish and Wildlife Service
- U.S. Geological Survey
- U.S. Environmental Protection Agency
- Upper Mississippi River Basin Association
- Missouri Department of Conservation
- Iowa Department of Natural Resources
- Minnesota Department of Natural Resources
- Wisconsin Department of Natural Resources
- Illinois Department of Natural Resources
- The Nature Conservancy
- Audubon of Minnesota, Iowa & Missouri

Upper Mississippi River Restoration  
Leading. Innovating. Partnering.

**24**


**ENVIRONMENTAL JUSTICE**



25




26




27



28

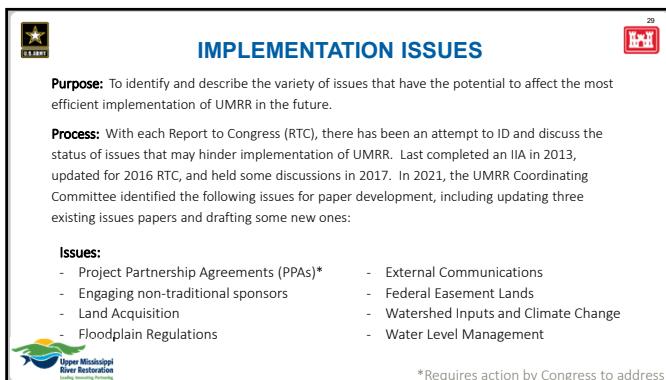

29

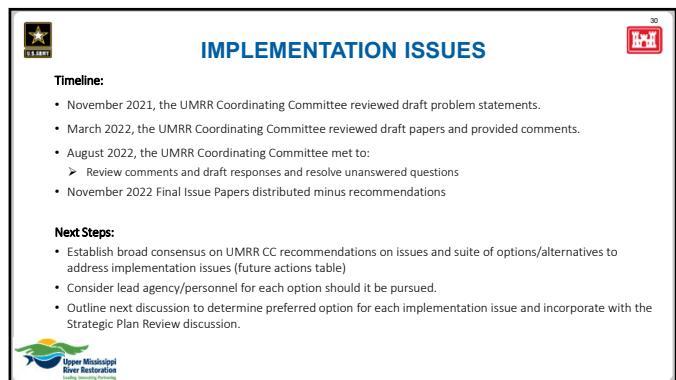

30

**2015 -2025 STRATEGIC AND OPERATIONAL PLAN REVIEW**



31

**2015 - 2025 STRATEGIC AND OPERATIONAL PLAN REVIEW**

- Draft Report nearing completion
- September 20, 2021, survey distributed to the UMRR partnership at-large regarding the 2015-2025 Strategic and Operational Plan.
- 200 individuals from state and federal agencies and non-governmental organizations involved in implementation of UMRR.
- Fifty-eight responses were received for a 29 percent response rate.
- The survey included questions about respondents' involvement with UMRR and their assessment of UMRR based on the Strategic Plan's four goals.
- Participants evaluated success criteria for three of the four goals.
- Participants prioritized actions meant to support each goal



32

**2015 - 2025 STRATEGIC AND OPERATIONAL PLAN REVIEW**

- Program Success
  - Goal 1** Enhance Habitat
    - ✓ Restoration projects provide opportunities for scientific research and inquiry
    - ✓ HREP enhance the health and resilience of the UMR
    - ✓ UMRR serves as a source of guidance on restoration for similar programs nationally
    - ✓ UMRR is recognized as a premier program in large river restoration
  - Goal 2** Advance Knowledge
    - ✓ Research and monitoring inform restoration and management efforts
    - ✓ UMRR is recognized as a premier program in large river monitoring and science
    - ✓ UMRR serves as a source of guidance on monitoring and science for similar programs nationally
    - ✓ UMRR effectively detects the status and trends of the UMR as related to indicators of ecosystem health and resilience
  - Goal 3** Communications
    - [no success criteria were available for Goal 3]
  - Goal 4** Partnership
    - ✓ The partnership is supportive of program and its output
    - ✓ UMRR has a highly engaged regional partnership



33

**2015 - 2025 STRATEGIC AND OPERATIONAL PLAN REVIEW**

- Priority Actions
  - Goal 1** Enhance Habitat
    - Centralize HREP data and collect and digitize historic data currently stored in computers and file cabinets
    - Establish consistent and standardized HREP monitoring
    - Complete HREP project evaluation reports (PERs) across districts
    - Define appropriate temporal and spatial scales for determining physical and biotic response of habitat project objectives
  - Goal 2** Advance Knowledge
    - Connect resilience concepts with ongoing and future restoration work
  - Goal 3** Communications
    - Link together habitat restoration projects with existing watershed projects and upstream contributors
  - Goal 4** Partnership
    - Create a narrative around missed restoration opportunities because of existing policies



34

**DISCUSSION**





35



## UMRR Status and Trends Report Long Rollout

November 16, 2022

1

### Long Rollout


UMRBA is coordinating development of a series of four 2-page flyers related to findings presented in the Ecological Status and Trends report and creating a plan for disseminating flyers to the UMRR partnership and media outlets.

Topics will include:

- ✓ Fisheries
- Floodplain forest loss (in design)
- Sedimentation (in review)
- Aquatic vegetation
- Water quality and nutrients

2

### Fisheries



Meeting Agenda Packet - Attachment C

3

### Development Process

- UMRBA drafts flyer content
- Report authors review draft content
- A-Team and COT review revised content
- Flyer sent for final design
- Submit final version to UMRR Coordinating Committee for endorsement

4

### Key Findings

**Fish Communities:** The river system continues to support diverse and abundant fishes. However, invasive carps have substantially affected the river ecosystem where they have become common.

**Forest Loss:** Floodplain Forest loss has occurred across most of the system.

**Water Quality:** Concentrations of nutrients, notably nitrogen and phosphorus, remain high, exceeding U.S. Environmental Protection Agency benchmarks. However, total phosphorus concentrations has declined in many of the studied river areas.

**Sedimentation:** TBD

**Aquatic Vegetation:** TBD

5

### Key Findings

**Sedimentation:** DRAFT

Sediment accumulation has changed the river structure by creating new floodplain land areas and reducing depths in backwater areas. These changes affect the quality and availability of habitat for fish and wildlife.

The loss of deep backwater areas can reduce suitable habitat for some fish species, especially for overwintering.

New landforms with sandy substrates can be important habitats for shorebirds and waterbirds and offer ideal conditions for the establishment of important tree species such as willows and cottonwoods.

7

## Key Findings

### Aquatic Vegetation: DRAFT

Aquatic vegetation diversity has improved in the Upper Impounded Reach of the Upper Mississippi River. However, aquatic vegetation diversity remains low or unknown in other reaches of the river.

Long-term monitoring reveals that improvements in aquatic vegetation are tied to lower nutrient loads in the water, better water clarity, and a decline in common carp.

The increase in submersed aquatic vegetation and water clarity in much of the Upper Impounded Reach represents a significant improvement in the ecological condition of the Upper Mississippi River System.

Aquatic vegetation helps sustain clearer water, provides important habitat for many aquatic animals, and is an important food source for migrating waterfowl

## Next Steps

### Next 2-page flyers:

- Floodplain forest loss (Complete design)
- Sedimentation (A-Team and COT review)

### Ongoing:

- Request for photos w/ photo credit information shared

## UMRR COMMUNICATION AND OUTREACH TEAM Update

Jill Bathke  
St. Paul District- Plan Formulation



1

## UMRR Joint Press Release Best Practices

- Developed & disseminated best practices based on 2022 Status and Trends Release

**Key Takeaways:**

**Participation**

- Identify key partners in press release and identify their needs early on
- Identify best dissemination and communication methods for non-UMRR river groups

**Messaging**

- Key message development, including accessibility and accuracy, is time well-spent**
- Keep language plain and clear
- Identify and confirm technical and/or communication prior to distribution of press release
- Develop a FAQ document before press release, if possible
- Tie key messages to areas of effect

**Press Relationships**

- Continue to build relationships with the Mississippi River Basin Ag & Water Desk




2

## UMRR Joint Press Release Best Practices

**Timing**

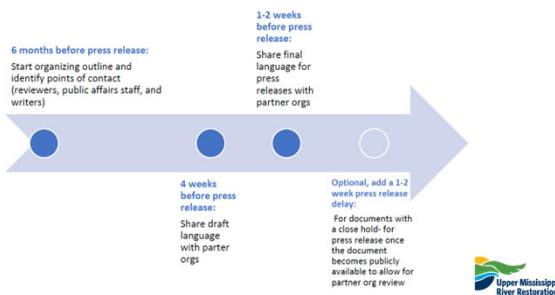

6 months before press release:  
Start organizing outline and identify points of contact (reviewers, public affairs staff, and writers)

4 weeks before press release:  
Share draft language with partner orgs

1-2 weeks before press release:  
Share final language for press releases with partner orgs

Optional, add a 1-2 week press release delay:  
For documents with a close hold for press release once the document becomes publicly available to allow for partner org review



3

## Winter 2023: COT Next Steps

- Encourage wider partner participation
- Cooperation with UMR NWFR 100<sup>th</sup> Anniversary Communications
- Communications surrounding 2022 UMRR Report to Congress
- Strategic Plan Update Communications
- UMRR video series
- Create communications inventory


4

## UMRR Communication and Outreach Team

**Points of Contact:**

Jill Bathke USACE-RPEDN-PD-F @ MVP <a href="mailto:Jill.C.Bathke@usace.army.mil">Jill.C.Bathke@usace.army.mil</a>	Rachel Perrine USACE-RPEDN-PD-F @ MVR <a href="mailto:Rachel.E.Perrine@usace.army.mil">Rachel.E.Perrine@usace.army.mil</a>
---	--




5

  
**LTRM FY22 Accomplishments**  
**Many Contributors!!!**

UMRR Coordinating Committee Meeting  
16 November 2022  
Presented by Jennie Sauer, USGS

1

**Status and Trends Report**

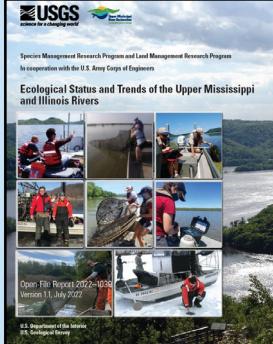

Published and printed!  
Media coverage!

**MPRnews**     
**WISCONSIN PUBLIC RADIO**  
**FarmWeek Now.com**  
**THE LENS** 

2

**LTRM Base Monitoring: Fisheries**

- Steve DeLain & Chris Dawald (MDNR), Andy Bartels & Kraig Hoff (WDNR), Travis Keuter (IDNR), Eric Gittinger, Eric Weyers, Levi Solomon, & Kris Maxson (INHS), Andrew Glen (MDC) and Brian Ickes (UMESC) Plus many technicians!
- 29th year of standardized sampling of the fish community and single species changes
- Low water the theme this year
- SVCP we saw very little reproduction
- Multiple publications



3

**Fall/Winter Work**



4



**LTRM Base Monitoring: Aquatic Vegetation**

- Eric Lund (MNDNR), Alicia Carhart (WIDNR), Seth Fopma (IADNR), Danelle Larson (USGS). Plus many technicians!
- 24<sup>th</sup> year of LTRM aquatic vegetation sampling
- Plant abundance and diversity generally remains high
- Invasive flowering rush populations increased dramatically since 2020.
- Multiple publications!

5

**LTRM veg. crews assisted with sampling design and additional monitoring of flowering**



Before (left) and after (right) foliar herbicide was applied to flowering rush stands

6

Pattern of Wild Rice Colonization and Retreat  
Dataset: Benjamin Finley (USGS)

- Created method for high-accuracy mapping of emergent vegetation using UAS assets
- Field work completed over lower-Pool 8 study areas
- Photo orthomosaic imagery created
- Formal spatial accuracy assessment ongoing
- Report on inter-decadal change in-progress

Task SD7

7

- Rob Burdis (MDNR), John Kalas (WDNR), Ashley Johnson (IDNR), Lori Soeken-Gittinger, Sara Sawicki (INHS), Luke Zuklic (MDC), and Kathi Jo Jankowski (UMESC). Plus many technicians!
- 28 years of data to capture spatially and temporally dynamic water quality changes in response to watershed changes
- In 2022, continued chloride monitoring and phytoplankton research
- Multiple publications

LTRM Base Monitoring: Water Quality

8

### Water Quality

- WQ analysis in lab on-going
- Successful upgrade of ScanLog/data transfer to sFTP (major kudos to Ben Schlifer)
- ~950 samples are set to be shipped to contractor for phytoplankton ID samples from 2007-2021

Quivre Lake (Sara Sawicki, INHS-IRBS)  
Marquette Island (Luke Zuklic, MDC, Big Rivers)

9



10

### LTRM WQ Laboratory

Xiaoli Yuan, John Manier, Derek Craig (USGS), and Technicians

More than 60,000 analyses run  
USGS Standard Reference  
Renovation and move to UW-L

Orthophosphate as P	
Excellent 0 – 0.5	
Good 0.51 – 1	
Satisfactory 1.01 – 1.5	
1	
0.5	
0	

11

### LTRM WQ Laboratory

Learn something new everyday!

- More than 320 Quality Control Reports completed

**Future generation: Part I**

- More than 60 interns through WQ lab the last 30 years
- Land O'Lakes
- National Park Service
- Minnesota Pollution Control Agency
- Sigma Aldrich
- Multiple PhD students

12

**Goal 3**  
**Engage and Collaborate with Other Organizations and Individuals to Help Accomplish the UMRR Vision**

- Brian Ickes (USGS) collaborating with agencies on newly planned ecological assessment programs on the Columbia and Hudson River systems




13

**Improving our understanding of historic, contemporary, and future UMRS hydrology**

Molly Van Appledorn, USGS UMESC and Lucie Sawyer, USACE MVR

- Database template developed for historic and contemporary daily water service elevations at UMRS USACE gages. ~95% of data
- Draft of the LTRM Report "UMRR Future Hydrology Meeting Series"



14

**Land Cover/Use (LCU) 2020 mapping**  
Erin Hoy, Julia (Rose) Bruce, Andrew Strassman, Janis Ruhser, Benjamin Finley (USGS)

- Pools 4, 8, 13, 26, Open River South completed and on-line.
- Pools 9, 12, and La Grange Pool under USGS review.
- Groundtruthing for Pools 1-3, 5-7, St Croix and MN River were completed




15

**Mapping Potential Sensitivity to Hydrogeomorphic Change in the UMRS Riverscape and Development of Supporting GIS Database and Query Tool**

Angus Vaughan, USGS UMESC; Faith Fitzpatrick, USGS Upper Midwest WSC; Jayme Strange, UMESC; Molly Van Appledorn, UMESC

- GIS-based analyses were successful at identifying a range of hydrogeomorphic units
- The approach was successfully piloted in Pools 8, 10, and Pool 14

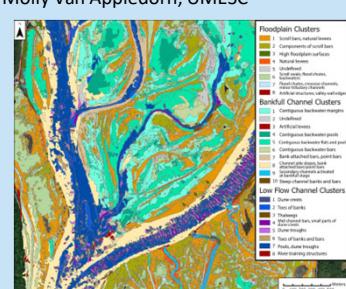

16

**Systematic analysis of hydrogeomorphic influences on native freshwater mussels**

Teresa Newton, Robert Francis, Danielle Schultz, Jason Rohweder, Nate DeJager, Nathan Johnson (USGS)


**Obj. 1. Estimate the distribution, abundance, diversity, and recruitment of native mussels in Pools 8 and 13**

- Quantitative systematic surveys completed
- Similar assemblage structure between pools

**Obj. 2: Identify geomorphic gradients using physical habitat metrics across six navigation pools**

- Analysis to assess variation in hydrogeomorphic metrics across spatial scales
- Variability in hydrogeomorphic metrics typically decreased with spatial scale


**Obj. 3. Assess if geomorphic indices are predictive of the distribution, abundance, diversity, and recruitment of native mussels across six pools**



17

**Refining our Upper Mississippi River's ecosystem states framework**

Danelle Larson, John Delaney, Jason Rohweder (UMESC), Alicia Carhart (WDNR), Wako Bungula (University of Wisconsin- La Crosse)

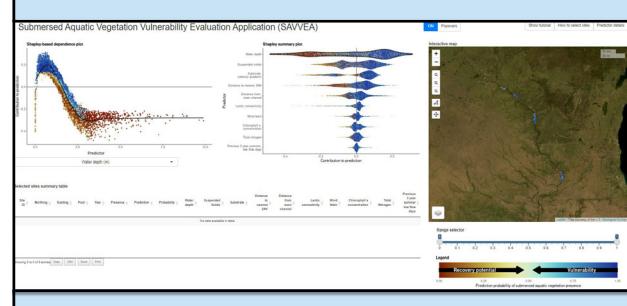


18

## UMRS Resilience Assessment

Kristen Bouska (UMESC)

- [New publication: Resisting-Accepting-Directing: Ecosystem Management Guided by an Ecological Resilience Assessment](#)

- Analysis of general & specified interactions underway
- “Lessons Learned & Future Directions” manuscript in prep



19

## Vital Rates, Genetics, and Microchemistry of UMRS Fishes

Andy Bartels (WDNR), Kristen Bouska (UMESC), Quinton Phelps (MSU), Greg Whithelde (SIU), Jim Lamer (IRBS), Mark Davis (UIUC), Milton Tan (UIUC), Jim Lamer (IRBS), Wes Larson (NOAA)

- Analyses wrapping up and manuscripts in preparation
  - Genetic analyses of regional species almost completed
  - Largemouth Bass vital rate publication in review
  - Natal origins paper to be submitted by Dec.
- Monthly meetings among PIs to develop synthesis paper and management report



20

## Future generation: Part II

Kylie B. Sterling – Spring 2022

- Largemouth Bass in the Upper Mississippi River: An Evaluation of Management Strategies and Understanding Potential Factors Influencing Dynamic Rate Functions
- Initial Employment: U.S. Geological Survey – Columbia, MO

Elaine Ewigman – Anticipated Fall/Winter 2022

- Population Dynamics and Habitat Use of Gizzard Shad *Dorosoma cepedianum* in the Upper Mississippi River
- Initial Employment: Oklahoma Dept. of Wildlife Conservation – Aquatic Nuisance Species Coordinator

Aaron Muehler – Anticipated Spring 2023


- Recruitment Dynamics of UMRS Fishes

21

## Understanding physical and ecological differences among side channels of the UMRS

Molly Sobotka (MDC), Kristen Bouska (UMESC), Todd Slack (ERDC), Heather Theel (ERDC), Ross VanderVorst (UWL)

- Manuscript on side channel classification based on fish associations with physical metrics currently in review
- Benthic invertebrate identification underway (UWL)



22

## Collaboration with HREPs

- All Lake City LTRM staff attended a meeting with Refuge Winona District Manager, Mary Stefanski, in March 2022 to share data and perspectives on Big Lake, Pool 4

- Initiated workgroup to develop a research proposal capitalizing on Learning Opportunities from Lower Pool 13 HREP PDT Bierman and Seth, Houser, Bouska

Photo Nicole Ward, MDNR

23

## Reno Bottoms Canoe Trail Access Patterns of forest regeneration following removal of invasive Reed Canarygrass under different simulated hydrological scenarios

Nathan R. De Jager, Jason J. Rohweder, Molly Van Appledorn, Enrika Hlavecek (UMESC), Andy Meier, Megan McGuire (USACE)

Used the Landis-II forest simulation model to project patterns of forest recruitment and succession with and without inhibition of forest regeneration in areas currently occupied by invasive Reed Canarygrass

Two different future 100-year hydrologic scenarios: a future like the past 40 years and a future with an increasing trend in flooding probability.

MEMORANDUM FOR Commanders, St. Paul, Rock Island, and St. Louis Districts, U.S. Army Corps of Engineers (Attn: Ms. Monique Savage, CEMVP-PD-F)

SUBJECT: Approval for Regional Use – LANDIS-II Forest Succession Model in the

24

13

**Upper Mississippi River Restoration Program**  
Long Term Resource Monitoring

Who We Are • Components • Data and Tools • Reports • UMRSC Search

Reports and Publications

Bouska, K. L., N. R. De Jager, and J. N. Houser. 2022. Resisting/Accepting/Dirting: Ecosystem management guided by an ecological resilience assessment. *Environmental Management*. <https://doi.org/10.1007/s00261-022-11657-y> *Abstract*

Bouska, K. L., M. Larson, D. C. Drake, E. M. Lund, A. N. Cartart, and K. R. Bates. 2022. Aquatic vegetation dynamics in the Upper Mississippi River over 2 decades spanning vegetation recovery. *Freshwater Science* 41:1. <https://www.journals.uchicago.edu/doi/10.1897/21-7857> Data available here: [Abstract](#)

Dieterman, D. J., S. A. Dean, C. R. Donald, and A. Herberg. 2022. Darter (Family: Percidae) Abundance in Deep-Water Habitats of the Upper Mississippi River. *Natural Areas Journal*, 42(2), 139-144. <https://doi.org/10.3375/21-16> *Abstract*

Houser, J.N., ed. 2022. Ecological status and trends of the Upper Mississippi and Illinois Rivers: U.S. Geological Survey Open-File Report 2022-1039, 199 p., <https://doi.org/10.3133/of20221039>.

Gatto, J.V., B. S. Iones, J. H. Chick. 2022. Evidence of alternative trophic pathways for fish consumers in a large river system in the face of invasion. *River Res Appl*.2022;1-12. DOI: 10.1002/rra.3992. [Abstract](#)

Shi, Y., K. L. Bouska, G. J. McKinney, W. Tokaji, A. Bartels, M. V. McPhee, and J. A. Larson. 2022. Gene flow influences the genomic architecture of local adaptation in six riverine fish species. *Molecular Ecology*. <https://doi.org/10.1111/mec.15127> *Abstract*

Solomon, L.E., A.F. Casper, K.A. Nason, J.T. Lamer, T.W. Ford, K.D. Bridgett, T. Holson, D. Perry, N.T. Grider, R.B. Hislebeck, T.R. Cook, K.S. Gross, M.A. McClelland and T.M. O'Hara. 2022. A Case Study of Large Floodplain River Restoration: Ten Decades of Monitoring the Merwin Preserve and Lessons Learned through Water Level Fluctuations and Uncontrolled Recolonization to a Large River. *Wetlands* 42, 59 (2022). <https://doi.org/10.1007/s11270-022-01938-3> *Abstract*

Windmiller-Campione, N.A., L. F. Reuling, M. Van Appledorn, D. M. Nielsen, and A. R. Meier. 2022. What is a stand? Assessing the variability of composition and structure in floodplain forest ecosystems across spatial scales in the upper Mississippi River. *Forest Ecology and Management*, Volume 503. <https://doi.org/10.1016/j.foreco.2022.129385> *Abstract*

25

## Presentations

Mississippi River Research Consortium

16th Annual Emiquon Science Symposium




26

**Skype a Scientist**  
Molly Van Appledorn (USGS)



- Connects professional scientists with students
- North East Regional School of Biotechnology and Agriscience, 10th grade biology class.
- Andover Elementary, 4th and 5th grade students in advanced science classes.

27



UMRR 2022  
Virtual Science  
Meeting

- > 100 participants
- USACE, USGS, USFWS, USDA
- MDNR, WDNR, IADNR, INHS, ILDNR, MDC, UMRBA, NGRREC
- UW-Madison, UW-La Crosse, Missouri State University, University of Minnesota
- National Audubon Society

28


## LTRM Implementation Planning



29

## Illinois Waterway Closure

Vessel traffic significantly reduced during 2020 lock closure

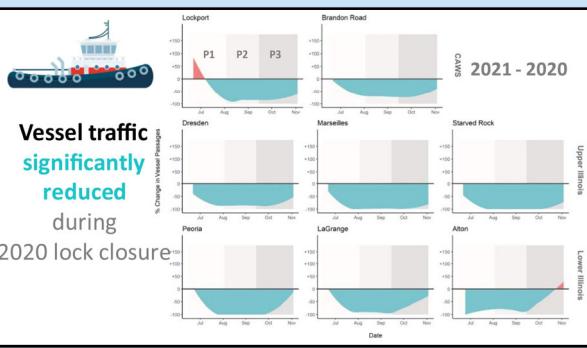

30



31

**FISCAL YEAR 2022 HABITAT REHABILITATION AND ENHANCEMENT PROJECTS ACCOMPLISHMENTS**

Angela Deen  
Julie Millhollin  
Brian Markert  
St. Paul District  
Rock Island District  
St. Louis District

16 November 2022

 US Army Corps of Engineers

**Upper Mississippi River Restoration**  
Leading. Innovating. Partnering.



1

**ST. PAUL DISTRICT FY22 ACCOMPLISHMENTS**



2

**THREE CONSTRUCTION COMPLETIONS**

➤ Harpers Slough HREP – Bass Ponds HREP – Conway Lake HREP



Kevin Wilson (DPM)   Conway Lake   Larry Quamme (Friends of Pool 9)   COL Jansen   Kristen Wallace (UMRBA)   Sabrina Chandler (USFWS)

3

**AWARDED STAGE II OF MCGREGOR LAKE**



**Proposed Project Features**

- River Mile
- Navigation Channel
- Floodplain Forest
- Stone Protection
- Wetland Protection
- Habitat Dredging

Features are subject to funding availability

4

**URBAN SHOWCASE – BASS PONDS HREP**

➤ UMRR-CC August Site Visit  
➤ River Resources Forum  
➤ Public Ribbon Cutting  
➤ Shakopee Mdewakaton Sioux





5

**SUCCESSFUL ISLAND REPAIR**

➤ Harpers Slough HREP





6

**PUBLIC AFFAIRS OFFICE STATS:**

**Featured projects/posts**

- Harpers/Conway ribbon cutting
- Bass Ponds ribbon cutting
- McGregor HREP
- Reno Bottoms HREP
- Big Lake HREP

**Video Analytics**

- 5 videos
- 7,926 views
- 637 reactions, comments and shares
- Reached 16,700 people

**Videos**

Harpers/Conway ribbon cutting: <https://www.facebook.com/usace.saintpaul/videos/143310160462228>  
 Bass Ponds ribbon cutting: <https://www.facebook.com/usace.saintpaul/videos/651959564969666>  
 McGregor construction video - interview: [https://www.youtube.com/watch?v=tH7z4f608P\\_4](https://www.youtube.com/watch?v=tH7z4f608P_4)  
 McGregor construction video - short: <https://www.facebook.com/usace.saintpaul/video/725486441900823>  
 Big Lake - interview: <https://www.youtube.com/watch?v=foJ9P8YN0Sc&t=1s6s>



**Social Media Analytics**

- Facebook, Instagram, LinkedIn and Twitter
- 88 posts
- #InvestInOurPlanet UMRR Earth Day campaign
- 32 posts across Facebook, Instagram, LinkedIn and Twitter




7

**APPLYING LESSONS LEARNED**



8

**APPLYING LESSONS LEARNED**

**Pigs Eye Lake**  
CAP 204 Project



**Upper Pool 4, Pierce County Islands**  
Section 1122 Pilot Project



**Upper Mississippi River Restoration**

9

**ROCK ISLAND DISTRICT FY22 ACCOMPLISHMENTS**



10

**ROCK ISLAND DISTRICT (MVR) ACCOMPLISHMENTS 2022**

**PLANNING**

Lower Pool 13, HREP, Pool 13, IA/IW

- Advanced feasibility study
- Finalized TSP and Completed DQCR

**Green Island HREP, Pool 13, IA**


- Advanced feasibility study

**Pool 12 Forestry HREP – Pool 12, IA/L/WI**

- Advanced feasibility study

**Quincy Bay HREP**

- Advanced feasibility study

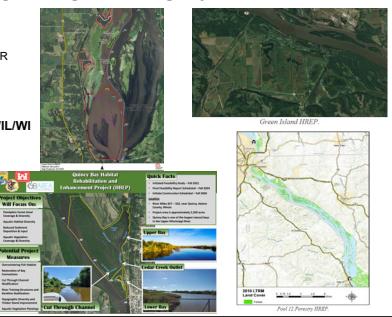

**Upper Mississippi River Restoration**

11

**ROCK ISLAND DISTRICT**

**Pool 12 Overwintering**

**Project Goals**

- Increase the amount of deep water habitat in the backwater lakes complex of Pool 12 to provide overwintering fish habitat.
- Provide aquatic habitat in the backwater lakes complex of Pool 12 by decreasing water levels in the lakes.
- Increase the amount of aquatic habitat in the backwater lakes complex of Pool 12 by decreasing water levels in the lakes.
- Increase area coverage in areas of forest stands with high potential for aquatic habitat component species in floodplain forest areas.
- Total project cost: \$20.7 million.

**Quick Facts**

- Location: Lower Pool 12, IA
- In Davies County, Illinois
- Project Area: 1,100 acres
- Number of lakes: 32.8 acres of aquatic and 31.4 acres of deep water habitat.
- Total project cost: \$20.7 million.

**Stage II: Stone & Tippy Lake**

**Stage I: Sunfish Lake**

**Monitoring**

Lake water monitoring station in Bellevue, IA has monitored pre- and post-construction water responses, to obtain data regarding Project impacts.

**Completed Work in FY22**

\*Turned over the project  
 \*Completed a ribbon cutting video





12

17



13

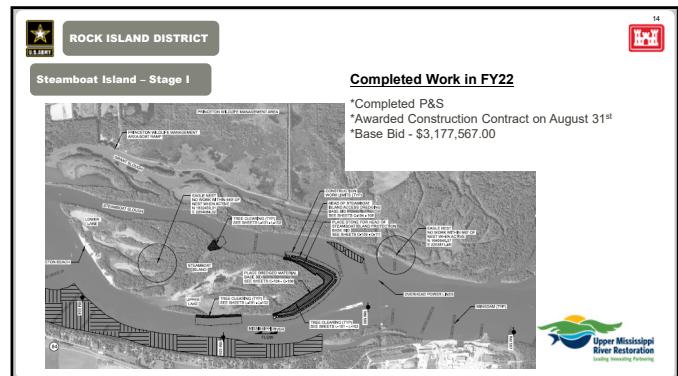


14



15



16

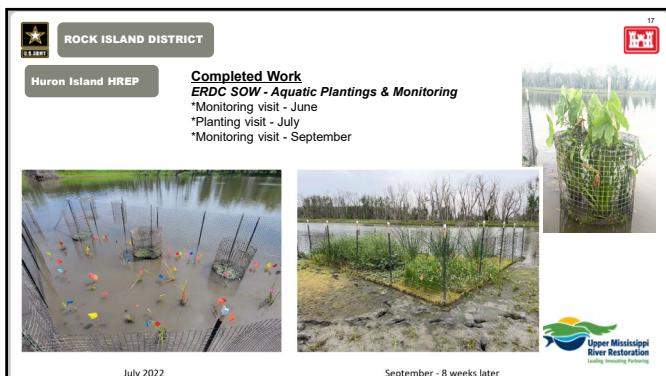

17



13

**ROCK ISLAND DISTRICT – UMR COMMUNICATIONS FY22**

**Featured Projects/Posts**

- River Action Visit to Beaver Island HREP
- UMRR #InvestInOurPlanet Earth Day Overview
- UMRR Celebrates 35 Years of History and Partnership
- President's Budget Announcement for UMR
- Long-Term Resource Monitoring Activities
- Harper's Slough Before/After Restoration
- Conway Lake/Harper's Slough Ribbon Cutting
- Keithsburg HREP
- Steamboat Island HREP
- Upper Miss. and Illinois River Status and Trends Report
- Pool 12 Overwintering HREP Ribbon Cutting
- Quincy Bay HREP Public Input Opportunity

**YouTube Videos**

- Three videos created in FY22
  - UMRR Celebrates 35 Years of History and Partnership
  - Pool 12 Overwintering HREP Virtual Ribbon Cutting
  - Quincy Bay HREP Public Input Opportunity
- Videos garnered 482 views, 9 'likes' and 28.8 hours of viewership

**Social Media Analytics**

- Facebook/Instagram
  - > 15,974 users reached
  - > 467 likes/reactions
  - > 16 comments
  - > 58 shares
- Twitter
  - > 2,490 users reached
  - > 117 engagements (likes, retweets, etc.)
  - #InvestInOurPlanet UMR Earth Week Campaign
  - > 12 posts across Facebook & Twitter
  - > 6,569 total users reached

**19**

**FACT SHEETS**

**MVR Result: 4 (of 5) Fact Sheets**

- ✓ Approved on September 2020 – Pool 18 Forestry HREP, Louisa and Des Moines Counties Iowa
- ✓ Approved on November 2020 – Lower Pool 11, Riverine, Backwater HREP, Wisconsin
- ✓ Approved on February 2022 – Multi Pool Habitat Protection, Pools 11, 12, 13, 14 and 17 HREP, Wisconsin, Iowa, Illinois
- ✓ Approved on January 2022 – Geneva and Hershey Island HREP, Muscatine, Iowa
- ✓ Not Approved – Upper Pool 13, HREP Jackson County, Iowa and Carroll and Jo Davies Counties, Illinois.

**Start a new project in 4<sup>th</sup> Quarter in FY23**

Tier 1 Projects – Multi-Pool Habitat Protection and Lower Pool 11  
 Tier 2 Projects – Upper Pool 13 and Geneva and Hershey Islands  
 Tier 3 Project – Pool 18 Forestry

**20**

**ST. LOUIS DISTRICT  
FY22 ACCOMPLISHMENTS**

**21**

**ADVANCED CONSTRUCTION - MVS AWARDED CONSTRUCTION CONTRACTS, TASK ORDERS, AND MODIFICATIONS**

**CONSTRUCTION**

**Crains Island, IL HREP (Open River)**

- Completed Sediment Deflection Berm, dike removals, and wetland excavation (Stage I), [Our first Open River Project](#)

**Clarence Cannon Refuge, MO (Pool 25)**

- Pump Station 99% complete
- Berm Setback 80% Complete

**Piasa & Eagles Nest, IL HREP (Pool 26)**

- Completed Stage I Construction

**22**

**ST. LOUIS DISTRICT**

**Clarence Cannon HREP Pump Station**

**23**

**ST. LOUIS DISTRICT**

**Berm Setback 80% Complete**

**Clarence Cannon HREP Berm Setback**

Sep 19, 2022 at 2:08:35 PM  
 Arnada MO 63330  
 United States

**24**

23

24




25




26



27

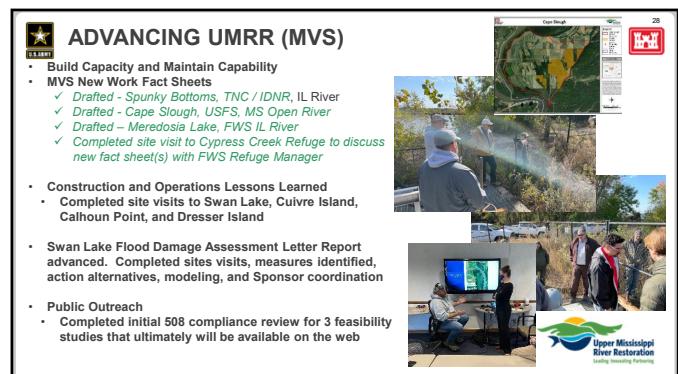


28




29




1

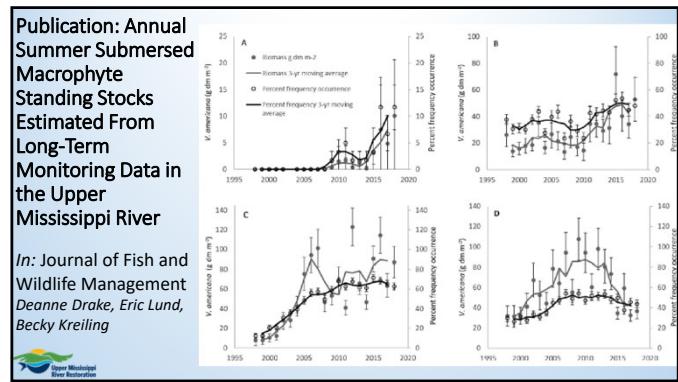

2

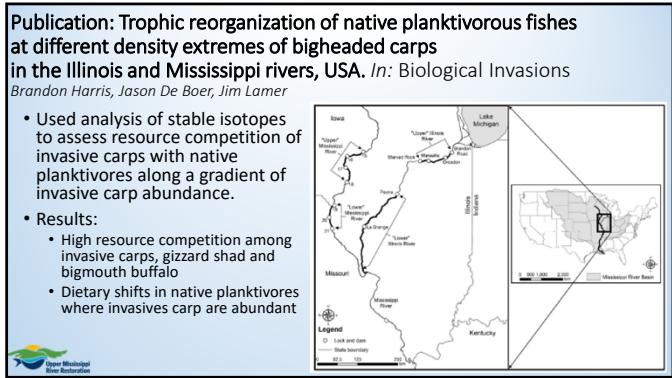

3

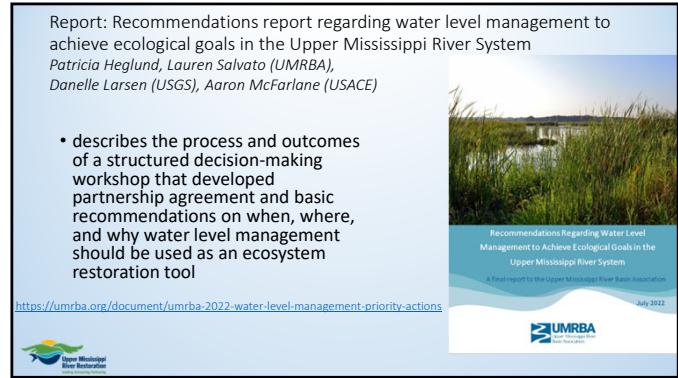

4



5

**UMRR MONITORING AND SCIENCE UPDATE**

Karen Hagerty  
Rock Island District  
16 November 2022

The views, opinions and findings contained in this report are those of the author(s) and should not be construed as official position, policy or decision, unless so designated by other official documentation.







**1**

**UMRR MONITORING & SCIENCE FY22**

**2 SOWs in FY22**

SOW for LTRM base monitoring  
**\$5.0M**

SOW for science in support (analysis under base)  
**\$1.3M**

**Both SOWs together are equivalent to a fully funded UMRR LTRM element \$6.3M**

**Science in Support of Restoration & Management**  
**\$2.5M**

**TOTAL: \$8.8M**



**2**

**UMRR MONITORING & SCIENCE FY23**

**\$33.17 Million UMRR Program**

**2 SOWs in FY23**

SOW for LTRM base monitoring  
**\$5.0M**

SOW for science in support (analysis under base)  
**\$1.3M**

**Both SOWs together are equivalent to a fully funded UMRR LTRM element \$6.3M**

**Science in Support of Restoration & Management**  
**\$2.5M**

**TOTAL: \$8.8M**



**3**

**UMRR MONITORING & SCIENCE FY23**

**\$55 Million UMRR Program**

**2 SOWs in FY23**

SOW for LTRM base monitoring  
**\$5.5M**

SOW for science in support (analysis under base)  
**\$1.5M**

**Both SOWs together are equivalent to a fully funded UMRR LTRM element \$7.0M**

**Science in Support of Restoration & Management**  
**\$6.85M**

**TOTAL: \$13.85M**



**4**

**UMRR MONITORING & SCIENCE FY23**

**LTRM**

	Budget (gross)
MN	\$793,118
WI	\$786,028
IA	\$532,987
Great Rivers (IL)	\$532,643
Big Rivers & Wetlands (MO)	\$542,474
IRBS (IL)	\$562,848
Equipment	\$233,986
Component meeting	\$ 10,571
<b>STATES TOTAL (-carry-in)</b>	<b>\$3,934,912</b>
<b>UMESC TOTAL</b>	<b>\$3,400,019</b>
Corps tech/science reps	\$ 63,000
<b>TOTAL FY23 LTRM BUDGET</b>	<b>\$7,397,931</b>



**5**

**UMRR MONITORING & SCIENCE FY23**

**Science in Support of Restoration and Management**

High priority items

A. LTRM balance	\$ 464,671
B. Ecohydrology	\$ 459,797
C. LCU processing (last year)	\$ 335,238
D. Proposal adjustments	\$ 28,884
E. Macroinvertebrate contaminants	\$ 77,483
F. Herbarium	\$ 21,000
G. Future landscape modeling	\$ 588,674

**Subtotal**  
**\$1,975,747\***



**6**



## UMRR MONITORING & SCIENCE FY23



### Science in Support of Restoration and Management

Remaining funds                           **\$4,900,000**

#### Other priority items


- A. Additional FS equipment, WQ lab
- B. Unfunded FY22 proposals
- C. Updating topobathy (w/NESP support)



## Analysis Team chair update

**Scott Gritters**  
**Fish Management Biologist**  
**Iowa Department of Natural Resources**  
**Bellevue, Iowa**

**Notes from October 25, 2022 meeting**



DNR IOWA  
DEPARTMENT OF NATURAL RESOURCES

1


## Getting A-team corner UTD

- We display information about the A-team on two different places on the web
- One run by the USGS (A-team corner)
- One run by the Corps (Rock Island Website)
- Discussed how to get UTD on all information displayed especially esp. on A-team corner
- Includes field station information, yearly highlights etc.,
- Some information out of date and of course covid influence

DNR IOWA  
DEPARTMENT OF NATURAL RESOURCES

2

## A-team corner



Upper Mississippi River Restoration Program  
Long Term Resource Monitoring

Who We Are Components Data and Tools Reports UMRSC Search


**Analysis Team**

The purpose of the Analysis Team (A-Team) is to address technical matters related to the implementation of the LTRM element. The A-Team consists of representatives of the same partner agencies that are members of the [Upper Mississippi River Restoration Coordinating Committee](#). All states and federal partners and members of the A-Team should be represented by a single individual. The major roles of the A-Team include a focus on technical and science questions related to LTRM.

Analysis Team Contacts  
Field Station Staff

3

## Corps Website



UMRR Coordinating Committee  
The UMRR Coordinating Committee (UMRR CC) is the primary consultative body used to discuss and seek consensus on UMRR budgetary, policy, and implementation issues.


MEETING DOCUMENTS

UMRR CC Meetings  
Date Location  
May 24, 2023 St Paul, MN

MEETING DOCUMENTS

A-Team Meetings  
Date Locations Time  
Oct 25, 2022, webinar 1:50 PM - 3:00 PM

4



USGS  
science for a changing world

Management implications of a resilience assessment of the Upper Mississippi River System


Kristen L. Bouska, Nathan R. De Jager, and Jeffrey N. Houser  
U.S. Geological Survey, Upper Midwest Environmental Sciences Center, La Crosse, WI

Photo credit: M. A.

U.S. Department of the Interior  
U.S. Geological Survey

5

## Resist-Accept-Direct (RAD)

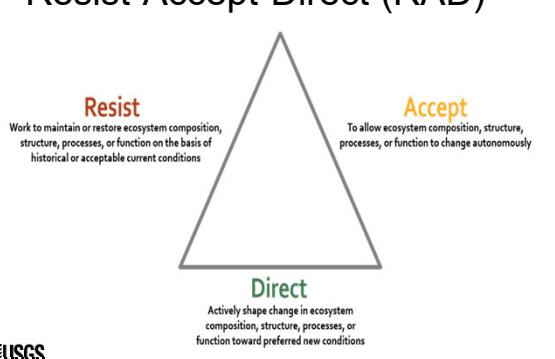

**Resist**  
Work to maintain or restore ecosystem composition, structure, processes, or function on the basis of historical or acceptable current conditions

**Accept**  
To allow ecosystem composition, structure, processes, or function to change autonomously

**Direct**  
Actively shape change in ecosystem composition, structure, processes, or function toward preferred new conditions

USGS

Adapted from Thompson et al. 202

6

## Conclusions

- Assessing resilience can aid in navigating the resist-accept-direct framework
  - General resilience
  - Distance to thresholds
  - Desirability of conditions
- Understanding trajectories of change and implications on ecological resources can aid in evaluating management actions under future scenarios




7

## 2022 Pool 13 Aquatic Vegetation Summary



Seth Fopma  
Iowa Department of Natural Resources  
Bellevue LTRM Station

8

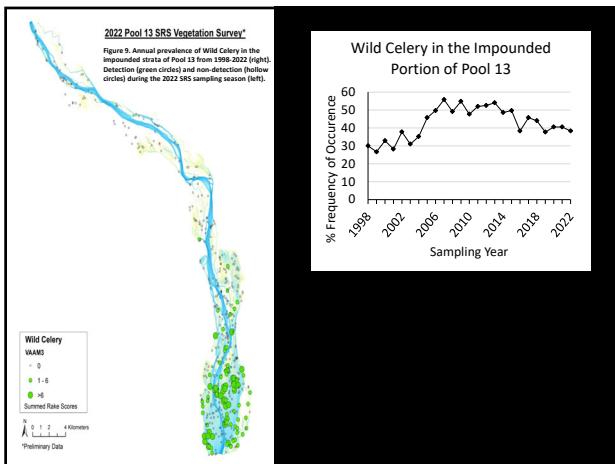

9


## How can A-team help with HREP/LTRM Integration?

- Long discussion
- Each situation HREP is different
- Make sure all on PDT's know what information is available
- Make sure in LTRM trend information is presented early on in the process
- Make sure the PDT's know that the A-team chair or reps will respond to any information needs



10

## UMRBA Brochures



**Upper Mississippi and Illinois Rivers Experience Widespread and Regional Changes in Fish Communities**


**25 Years of Monitoring and Research Show the Fish Community Remains Resilient but Faces New and Ongoing Stressors**

**Challenges to a Healthy Fish Community**

The fish community is diverse and function despite impacts from human activity and environmental changes. The river is home to at least 143 fish species and continues to

11

## Field Station in Focus

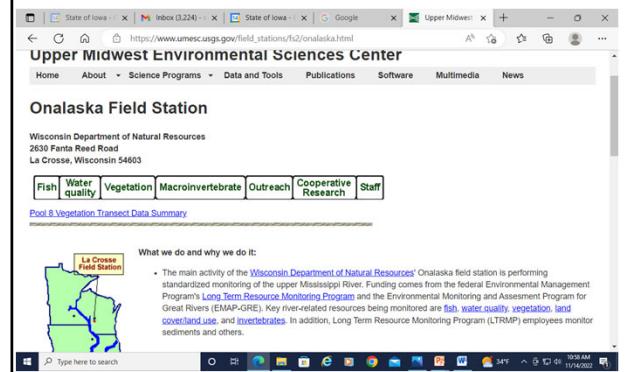

**Upper Midwest Environmental Sciences Center**

**Onalaska Field Station**

Wisconsin Department of Natural Resources  
2630 Fanta Reed Road  
La Crosse, Wisconsin 54603

**Fish Water quality Vegetation Macroinvertebrate Outreach Cooperative Research Staff**

**Pool 8 Vegetation Transect Data Summary**

What we do and why we do it:

The main activity of the Wisconsin Department of Natural Resources' Onalaska field station is performing long-term monitoring of the Upper Mississippi River. This is part of the Federal Interagency Monitoring Program's Long-Term Resource Monitoring Program and the Environmental Monitoring and Assessment Program for Great Rivers (EMAP-GRE). Key river-related resources being monitored are fish, water quality, vegetation, land cover/land use, and invertebrates. In addition, Long Term Resource Monitoring Program (LTRMP) employees monitor sediments and others.

12



13

# UMRR LTRM Implementation Planning Update

UMRR Coordinating Committee Quarterly Meeting

16 November 2022

Davenport, Iowa



1

## Implementation Planning

Why? To prepare for potential increased funding resulting from increased UMRR authorization under WRDA 2020.

Goal: Develop a set of portfolios of actions that best address UMRR management and restoration information needs.

Examples of possible new work include (but are not limited to):

- Short-term, focused research studies
- Increased capacity for analysis of existing LTRM data
- Spatial expansion of baseline monitoring (and associated analyses)
- Addition of long-term monitoring components (and associated analyses)



2

## Progress

- Formation of Implementation Planning Group and selection of facilitators
- **March 2022:** Bi-weekly meetings begin
  - Agree on Opportunity Statement
  - Draft Restoration and Management Information needs for the UMRS
  - Draft criteria for assessing information needs.
- **13-15 September:** In-person workshop:
  - Review revisions of information needs document
  - Agree on initial working draft of criteria
  - Discuss and test approach for prioritization of information needs and optimization of portfolios of work.
- **28 October:** Information needs [D-16] and scoring criteria finalized [D-37]
- **10 November:** Scoring of information needs submitted to facilitators



3

## Categories of Information Needs [D-16]

- Floodplain ecology
- Hydrogeomorphic change
- Aquatic ecology
- Restoration applications



4

## Example Information Needs [D-16]

### Floodplain Ecology

- Vegetation change across the system
- Distribution of birds and bats

### Hydrogeomorphic change:

- Geomorphic trends
- Evaluation of large woody debris source, transport, and fate

### Aquatic ecology

- Mussel distribution
  - River gradients
- Restoration Applications**
- Floodplain vegetation change at the HREP scale
  - Soil dynamics and ecosystem processes at the HREP scale



5

## Criteria for assessing Information Needs [D-37]

- Relevance/Importance to Ecosystem Understanding and Assessment
- Relevance/Importance to Management and Restoration
- Depth of Current Knowledge (less current knowledge -> higher score)
- Opportunity to Learn
- Urgency
- Unique capacity



6

## Next steps [D-15]

- **10 November** – Deadline for submitting scoring of information needs to facilitators
- **17 November** – Facilitators present, and group discusses, results of second round of information need scoring
- **5 December.** Initial, *approximate estimates* of costs of addressing each information need.
- TBD: Optimization of Information Needs based on criteria score and estimated costs.
- TBD: Portfolio development



7

## Implementation Planning Group

- |  |  |
|--|--|
| <ul style="list-style-type: none"><li>• Kirk Hansen IADNR</li><li>• Jim Lamer IRBS</li><li>• Molly Sobotka MDC</li><li>• Matt Vitello MDC</li><li>• Rob Burdis MDNR</li><li>• Nick Schlesser MDNR</li><li>• Neil Rude MDNR</li><li>• Andrew Stephenson UMRBA</li><li>• Davi Michl USACE</li><li>• Rob Cosgriff USACE</li></ul> | <ul style="list-style-type: none"><li>• Karen Hagerty USACE</li><li>• Matt Mangan USFWS</li><li>• Steve Winter USFWS</li><li>• Kristen Bouska USGS</li><li>• Nate De Jager USGS</li><li>• Jeff Houser USGS</li><li>• Jennie Sauer USGS</li><li>• Robb Jacobsen USGS</li><li>• Jim Fischer WDNR</li><li>• Madeline Magee WDNR</li></ul> |
|--|--|

Facilitators:  
David Smith (USGS)  
Max Post van der Burg (USGS)



8

**HABITAT RESTORATION – DISTRICT REPORTS**

36

**ST. PAUL DISTRICT (MVP)**

**PLANNING**

- Robinson Lake – Pool 4, MN
  - Planning kick-off
- Big Lake – Pool 4, MN/WI
  - Initial alternatives, preliminary cost estimates
  - Public Meeting (Aug)
- Reno Bottoms HREP – Pool 9, MN/IA
  - Completed Draft Report
  - Released for Public Review
  - Public Meeting (Nov 3)
- Lower Pool 10 HREP – Pool 10, IA
  - Completed Scope of Work
  - Value Engineering Study
  - Agency & AE Site Visit

**CONSTRUCTION**

- Harpers Slough HREP – Pool 9, IA
  - Construction Complete, O&M Manual
- Bass Ponds, Marsh & Wetland HREP – MN River
  - Construction Complete, O&M Manual
  - Dedication Event (Oct 11)
- Conway Lake HREP – Pool 9, IA
  - Construction Complete, O&M Manual
- McGregor Lake HREP – Pool 9, WI
  - Stage I: 80% Complete
  - Stage II: Awarded base bid (Sept)

**Other Activities**

- Trempealeau Letter Report
- Outreach

37

36

**CURRENT HREP PROJECTS**

38

**PLANNING**

**Big Lake HREP**

**Reno Bottoms HREP**

39

38

**DESIGN**

**Lower Pool 10**

40

**CONSTRUCTION**

**McGregor Lake**

41

29

**ROCK ISLAND DISTRICT (MVR)**

**PLANNING**

- Pool 12 Forestry – Pool 12, IA/IL/WI
  - PDT had a site visit on Oct 26<sup>th</sup> (photos)
  - PDT is working on finalizing the alternatives
- Green Island – Pool 13, IA
  - PDT finalizing cost
- Lower Pool 13 – Pool 13, IA/IL
  - ATR – Started on Oct 17<sup>th</sup> – PDT back checking comments
  - Public Review started Nov 7<sup>th</sup>
  - Virtual Public Q&A Webex is scheduled for Nov 17<sup>th</sup> @ 4pm
- Quincy Bay – Pool 21, IL
  - PDT had an alternatives workshop on Nov 2<sup>nd</sup> (photos)
  - PDT has concurrence on the final array of alternatives

**DESIGN**

- Steamboat Island Stage II – Pool 14, IA/IL
  - 35% DDC/BCOE – completed
  - 65% DDC/BCOE – scheduled to start in Jan

**CONSTRUCTION**

- Pool 12 Overwintering, Pool 12, IL
  - Turned project over
- Beaver Island Stage IB, Pool 14, IA/IL
  - Contractor working on cleaning up the channel (Photos)
- Steamboat Island Stage I – Pool 14, IA/IL
  - Awarded contract on Aug 31<sup>st</sup>
  - Contractor working on submittals
- Keensburg Division Stage I, Pool 18, IL
  - Construction started on the next 500' of the spillway
- Keensburg Division Stage II, Pool 18, IL
  - Finishing the concrete walls on the storage building
  - Storage building scheduled to arrive on-site Nov 22<sup>nd</sup>
- Huron Island, Stage III - ERDC, Pool 18, IA
  - Ribbon cutting completed on Sep 7<sup>th</sup>

**FACTSHEETS**

- Still addressing sponsor comments on Upper Pool 13

42

**ROCK ISLAND DISTRICT**

**Pool 12 Forestry Site Visit**

**Quincy Bay Workshop**

43

**ROCK ISLAND DISTRICT**

**Beaver Island**

Tree Planting

Loading Truck at Blue Bell West

Blue Bell West Placement Site

44

**MVR HREP PROJECTS**

45

**ST. LOUIS DISTRICT (MVS)**

**PLANNING –**

- West Alton Islands, MO, HREP (Pool 26)
  - Continue Feasibility Planning
  - H&H modeling nearing completion
  - Sponsor meeting scheduled
- Yorkinut Slough, IL HREP (IL River)
  - Continue Feasibility Planning, Site Visit Scheduled
  - Finishing cost for ICA and draft TSP
- Piasa & Eagles Nest, IL HREP (Pool 26)
  - Hydraulic Channel Excavation
  - P&S Complete 4<sup>th</sup> Quarter FY22
- Harlow Island, IL HREP (Open River)
  - Initiate Stage 2, P&S 1<sup>st</sup> Quarter FY23
- Oakwood Bottoms, IL, HREP (Open River)
  - Complete 4 P&S packages 1<sup>st</sup> & 2<sup>nd</sup> Quarter FY23
  - Pump Station, Well Pumps, North & South Units
  - Earthwork & Water Control Structures

**CONSTRUCTION –**

- Crains Island, IL HREP (Open River)
  - Stage 2, P&S Update 2<sup>nd</sup> & 3<sup>rd</sup> Quarter FY23
- Crains Island, IL HREP (Open River)
  - Channel Cleanout Acquisition
- Piasa & Eagles Nest, IL HREP (Pool 26)
  - Stage II – Pre-Solicitation issued 26 Oct
  - Contract Award and Task Order 1 Issue
  - Anticipated early 2<sup>nd</sup> Quarter FY23
- Clarence Cannon Refuge, MO (Pool 25)
  - Exterior Berm (Levee) Setback Continues

**Other Activities**

- FS, INDR/INC, FWS - New Fact Sheets Drafted
- Letters of Support / Endorsement
- Swan Lake Flood Damage Assessment
- Letter Report Draft 2<sup>nd</sup> Quarter FY23

46

**MVS HREP PROJECTS**

47




1



2




3

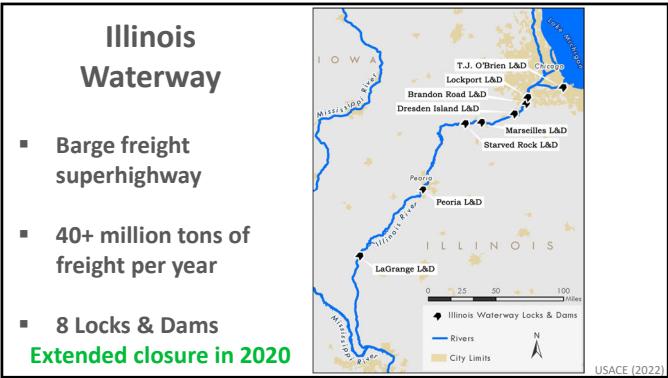


4




5

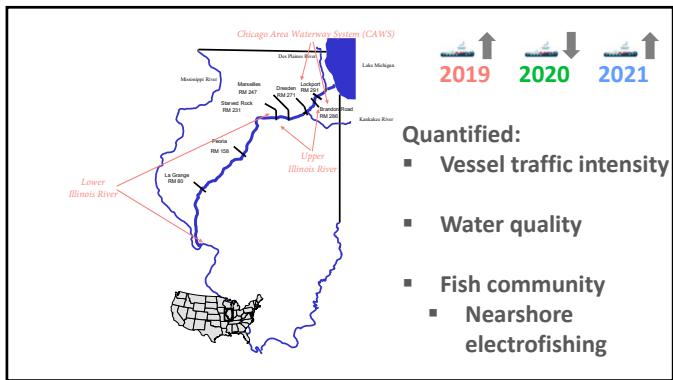


6

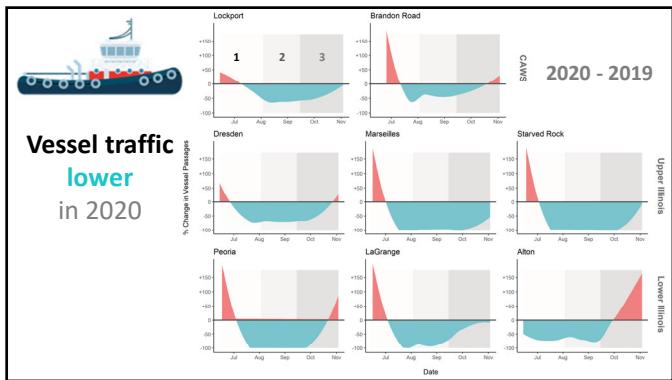


7

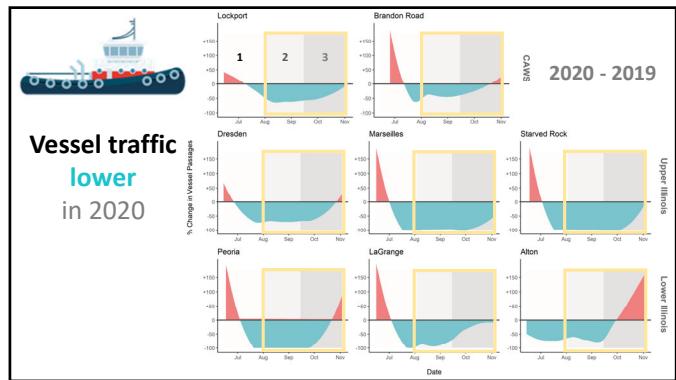


8

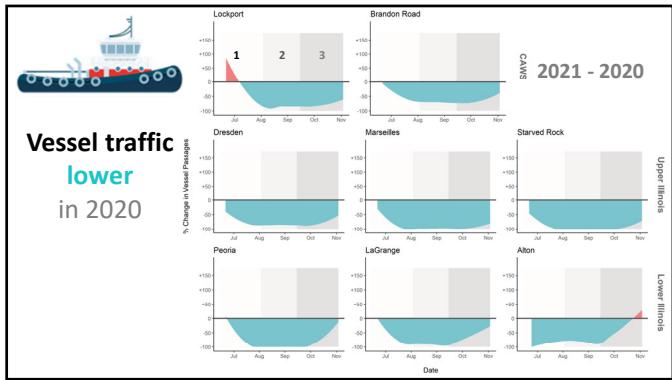


9

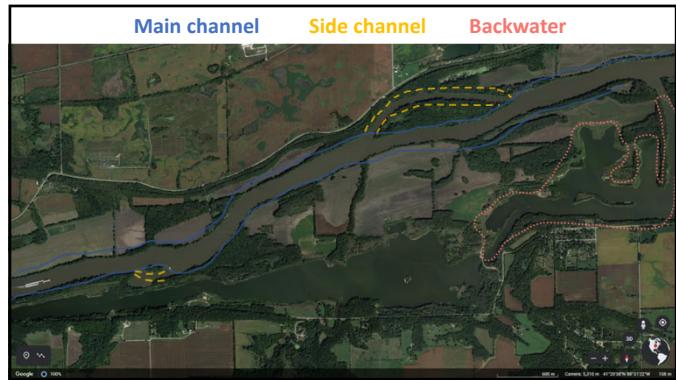


10

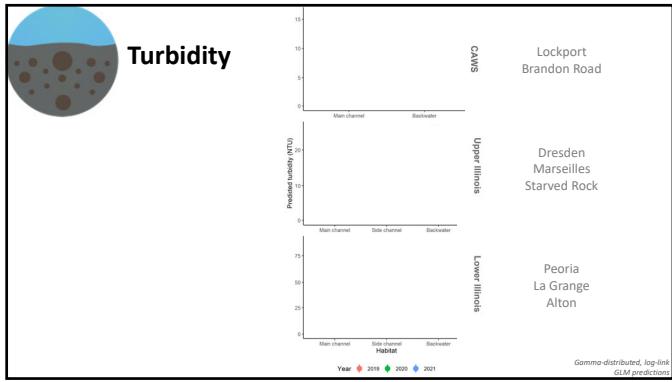

11

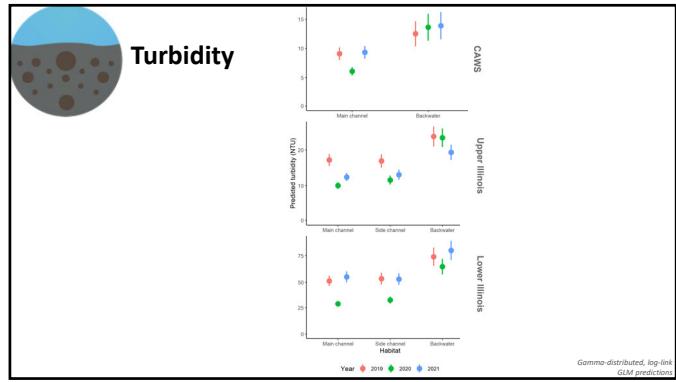


12

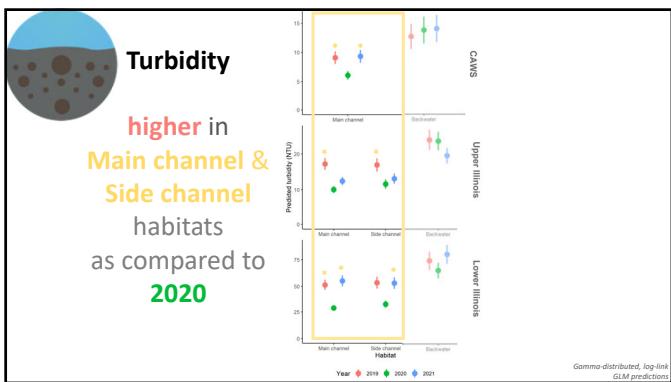


13




14

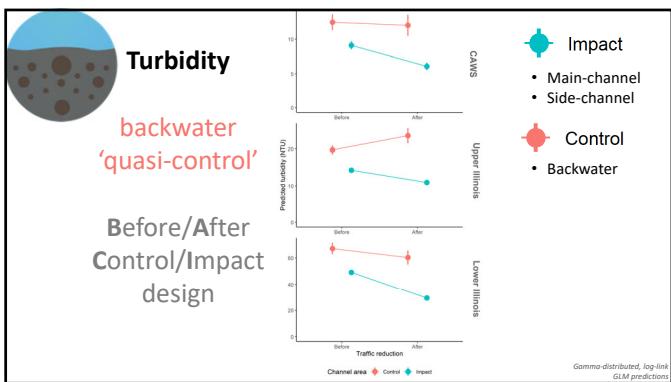


15

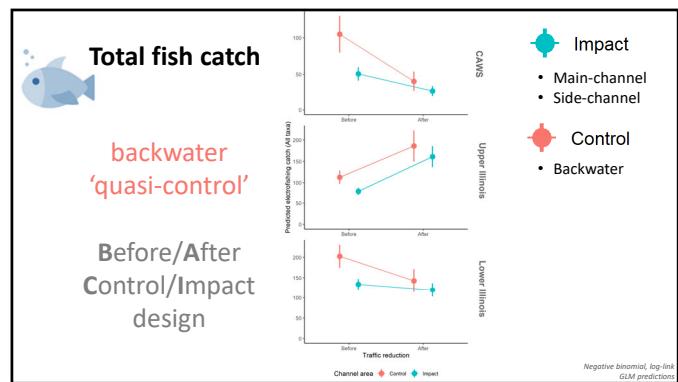


16

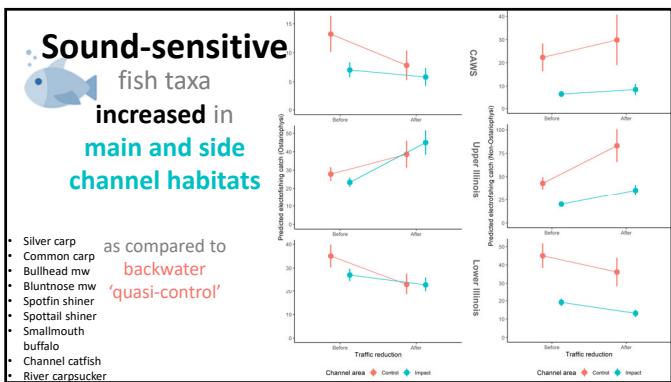

17

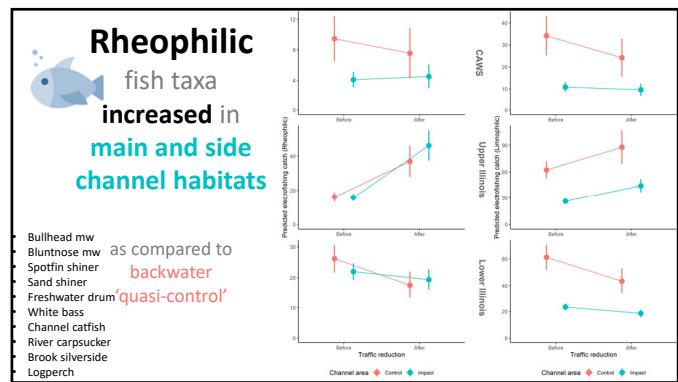

18

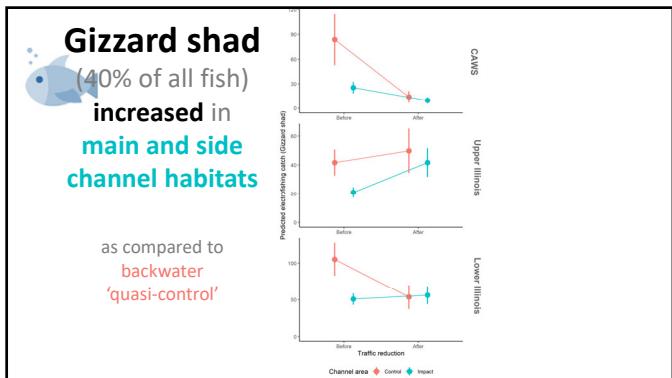


19

## Takeaways

- **Extended closure of locks and dams in 2020**
  - Ecosystem-scale opportunity to assess anthropogenic impacts of vessel traffic to a large river


20

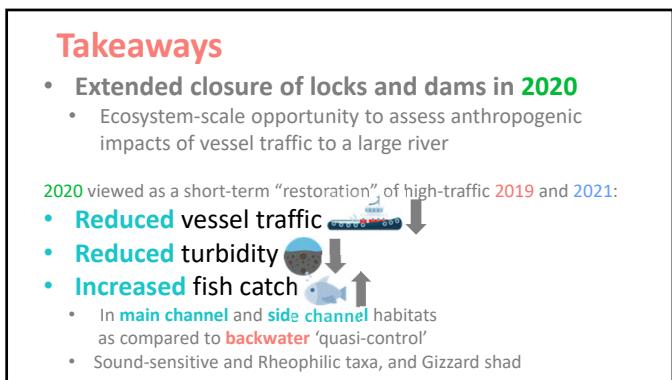


21



22

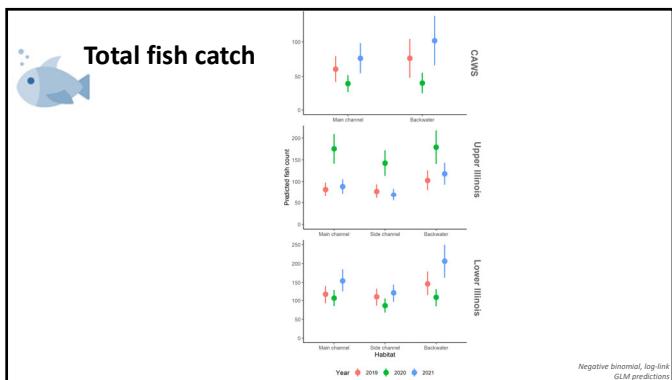

23

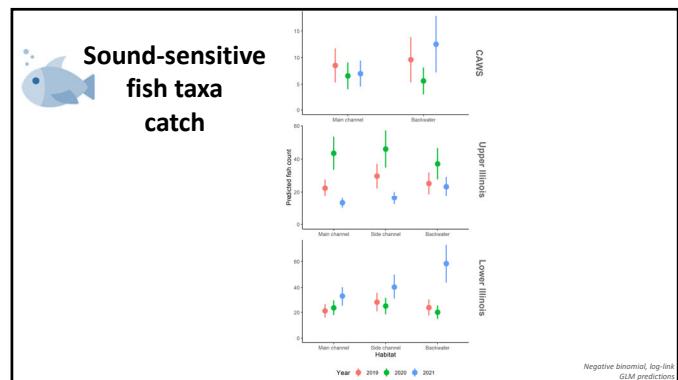

24

**Huron Island Complex  
Habitat Rehabilitation and Enhancement  
Project – Aquatic Vegetation Update**

Lynde L. Dodd<sup>1</sup>, Ricardo Luna<sup>1</sup>, Aaron Schad<sup>1</sup>,  
and Collin Moratz<sup>2</sup>

Leveeless Aquatic Ecosystem Research Facility  
Rock Island District

UMRCC Quarterly Meeting  
11/16/2022

<sup>1</sup>Research Biologist, Leveeless Aquatic Ecosystem Research Facility, U.S. Army Engineer Research and Development Center (ERDC), Leveeless, TX; [lynde.l.dodd@usace.army.mil](mailto:lynde.l.dodd@usace.army.mil); [www.erdc.usace.army.mil/leveeless/](http://www.erdc.usace.army.mil/leveeless/)  
<sup>2</sup>Interdisciplinary, Regional Planning and Environment Division, North at Rock Island District, Rock Island, IL; [collin.moratz@usace.army.mil](mailto:collin.moratz@usace.army.mil)

**ERDC**  
U.S. Army Corps of Engineers • Innovative solutions for a safer, better world

1

**Huron Island, Goose Lake – Establish, Monitor, and AM of Native Aquatic Vegetation –**

Location: Rock Island District, Pool 18, Upper Mississippi River Mile, Des Moines County, Iowa  
Purpose: Restore backwater habitat by excavating channels 8–ft. below flat pool, Goal: Provide overwintering/year-round fish habitat  
Authorization: Upper Mississippi River Restoration Program (UMRRP) under WRDA 1986  
Project Features:  

- Construct bathymetric and topographic diversity adjacent to and in backwater areas;
- Construct topographic diversity in non-diverse forested areas;
- Establish native aquatic and floodplain forest vegetation;
- Create a closure structure in Garner Chute; and
- Protect small side channel island and bankline protection in Huron Chute from erosion.

**ERDC Support:**  

- Develop and implement 3-Year aquatic vegetation establishment plan (~6 acres, > 1 mile shr.)
- Use flood tolerant native plant species of regional provenance
- Monitor employing adaptive management strategies 2-Years

**Progress to date:**  

- FY18 – Site evaluation and propagule collection/initiate culture
- FY19 – Propagule collection, propagation/initial plantings
- FY20 – Monitor, continue propagation/culture
- FY21 – Monitor, cont. prop./culture maint. and outplantings, FY21 Report
- FY22 – Monitor/AM vegetation community development, continue supplemental propagation and outplantings

**FY22 – Monitor/AM vegetation community development, supplemental propagation/culture maintenance and outplantings – Update to MVR**

US Army Corps of Engineers • Engineer Research and Development Center

2

**FY18–FY20 ERDC support:**

**FY18** – Initial site evaluation, planting plan, propagule collection, begin culturing plants  

- 20 species collected, 15 cultured

**FY19** – Additional propagule collection, propagation/production, initial plantings  

- August 2019 – herbivory exclosures installed (40)  
  - 15 spp. (~385 containers)
  - Delays/reduced effort from flooding

**FY20** – Monitoring, continued propagation/culture maintenance and outplantings; FY20 Report  

- Continued delays (COVID)
- September 2020 Assessment/Planting  
  - Some mortality due to 2019 flooding BUT waterlily, pondweed, spikerush, arrowhead establishing outside excl. (8-50% in excl.)
  - 11 species (~140 containers) planted, excl. repaired/repositioned
- Propagule collection – culture  
  - Vallisneria americana*

US Army Corps of Engineers • Engineer Research and Development Center

3

**FY21 ERDC support:**

**FY21** – Monitor/AM vegetation community development, cont. prop./culture maint. and outplantings, FY21 Report  

- Continue propagation/culture
- June 2021 Assessment  
  - Unprotected arrowhead recruitment
  - Spread of PONO from excl.
  - Good to high survival in exclosures (10 spp.)
- July 2021 Planting  
  - Large effort - 12 spp. (~425 containers)
  - New locations near mouth
- September 2021 Assessment/Planting  
  - Cutgrass obscured shoreline, BUT rushes and arrowheads observed unprotected
  - High survival in exclosures (13 spp.)

US Army Corps of Engineers • Engineer Research and Development Center

4

**Table 1. Results of native aquatic vegetation establishment efforts for MVR UMRRP Pool 18 Huron Island revegetation. NWPL = Midwest region - all species are CBL. \* annual species mixed with perennial submersed species. Area in m<sup>2</sup> given for installed protected and unprotected transplants, lateral spread, and recruitment of established species as of September 2021.**

Species	Common name	USDA Code	Habit	Protected				Unprotected				Spread/Recruitment				
				Installed Exclosure	m <sup>2</sup>	Transplants Exclosure	m <sup>2</sup>	Sept 2021 Plants	+	Transplants Plants	m <sup>2</sup>	Sept 2021 Plants	Column, % increase	Factor (X)		
<i>Alliaria cordata</i>	American water plantain	ALSI	Emergent	7	2.0	0	0	0	7.06	0	0					
<i>Bolboschoenus fluviatilis</i>	River bulrush	BOFL	Emergent	6	1.8	0.1	3	0.9	0.18	33	0.13	2	0.003	79	394	
<i>Eleocharis acicularis</i>	Needle spikerush	ELAC	Emergent	12	3.5	0.1	6	1.8	1.13	+	73	0.59	1	0	4	6
<i>Ludwigia peploides</i>	Floating primrose-willow	LUPE	Emergent	14	4.1	0.1	5	1.5	0.26	43	0.25	0	0	0	0	
<i>Pontederia cordata</i>	Pondweed	POCO	Emergent	12	3.5	0	34	9.9	1.32	+	30	0.06	0	0	0	0
<i>Sagittaria latifolia</i>	Scouring-rush arrowhead	SALA	Emergent	6	1.8	0	1	0.3	0.29	+	47	0.23	11	0.046	238	918
<i>Sagittaria trifolia</i>	Arrowhead	SATR	Emergent	20	5.8	0.1	3	0.3	0.03	+	30	0.07	0	0	0	0
<i>Schoenoplectus americanus</i>	Softstem bulrush	SCTA	Emergent	9	2.6	0.1	3	0.9	0.15	+	41	0.33	0	0.024	21	52
<i>Sporangium erycrautum</i>	Broadleaf bur-reed	SPBU	Emergent	2	0.6	0	6	1.8	0.75	+	21	0.17	1	0	8	43
<i>Nymphaea odorata</i>	American white waterlily	NYOD	Floating-leaved	22	14.4	0.2	11	2.0	6.01	+	54	0.44	24	0.219	19	31
<i>Cephalanthus occidentalis</i>	Common buttonbush	CEOC	Riparian	10	6.6	0.1	6	3.9	1.41	20	0.16	0	0	0	0	
<i>Elaeis canadenis</i>	Canadian waterlettuce	ELCA	Submersed	20	13.1	0.3	7	4.6	2.82	32	0.09	0	0	0	0	
<i>Patampogon nodosus</i>	Longleaf pondweed	PONO	Submersed	83	54.5	1.1	34	22.3	16.18	+	54	0.48	4	0.006	191	123
<i>Patampogon pusillus</i>	Small pondweed	POPU	Submersed	**	**	**	**	**	**	0	0	0	0	**	ma	
<i>Vallisneria americana</i>	American eelgrass	VAAM	Submersed	32	21.0	0.3	17	5.2	3.61	52	0.42	0	0.003	m	m	
Total	258	138.3	2.5	134	66.4	26.4	537	3.6	54	0.982	562	92				
Difference				53%	49%	1448%		10%	5%							

\*Non-perennial species (excludes subsp.)  
\*\*Patampogon pusillus (Small pondweed)

US Army Corps of Engineers • Engineer Research and Development Center

5

**FY22 ERDC support:**

**FY22** – Monitoring/AM of aquatic vegetation  

- Native plant culture maintenance/propagation at LAERF
- Vegetation establishment monitoring – assessments 6/28 and 9/21
- Supplemental protected outplantings (pen installations) 7/27
- Project updates to MVR; SOW for continued monitoring
- June - 25-90% cover protected eelgrass, unprotected colonies emergent (bulrush, arrowheads, bur-reed) and SAV (water lilies); recruitment (via seeds or fragments) of emergent (bulrush, arrowhead, bur-reed) and SAV (waterlily and pondweeds)
- July – Demonstrate methods to increase emergent/SAV cover by installing larger protective exclosures (Schad et al. 2021)

**Native Aquatic Plant Establishment Efforts in a High-Herbivore, Central Texas Reservoir**

Journal of Water Resources Protection, 2022, 16, 100-102  
DOI: 10.1002/jwr3.10012  
© 2022 Wiley Periodicals LLC  
Published online in Wiley Online Library (wileyonlinelibrary.com) on 10 June 2022

Aaron N. Schad • Brett J. Bellinger • Lynda L. Dodd • Jason Kelly • Kristina Hollingsworth • Gary D. Dick • Scott E. Allanson

Lake Austin, TX

US Army Corps of Engineers • Engineer Research and Development Center

## FY22 ERDC support:


- FY22 – Field campaign ERIC + MVR + DNR – July 26-28, 2022**

  - Supplemental planting – 11 spp. (~223 containers)
  - Installed 5 - 100' ft perimeter pentagonal, 2' x 2' mesh, 5-ft tall pens around SAV exc. to encourage spread – also planted with emergent
  - Replanted empty exc. (SAV/EV), moved deeper exc. shallower, repaired damaged exc.
  - EV exc., replanted with one container of either river bulrush, softstem bulrush, and bur-reed.
    - installed additional rebar needed to stabilize cages and repaired lids as needed
  - SAV exc. replanted with one container of either American eelgrass and longleaf pondweed.

Total number of plants outplanted July 2022 * 3 containers planted in each pen		
Species	Common name	Qty
<i>Bolboschoenus fluviatilis</i>	River bulrush	10*
<i>Eleocharis acicularis</i>	Needle spikelet	30*
<i>Equisetum laevigatum</i>	Carex-like horsetail	15*
<i>Ludwigia peploides</i>	Floating primrose-willow	15*
<i>Nymphaea odorata</i>	American white waterlily	15*
<i>Pontederia cordata</i>	Pickweed	15*
<i>Potamogeton pectinatus</i>	Long-leaf pondweed	20*
<i>Sagittaria latifolia</i>	Broadleaf arrowhead	15*
<i>Schoenoplectus tabernaemontani</i>	Softstem bulrush	20*
<i>Sporangium europeum</i>	Broadfruit bul-reed	20*
<i>Vallisneria americana</i>	American eelgrass	10*



US Army Corps of Engineers • Engineer Research and Development Center

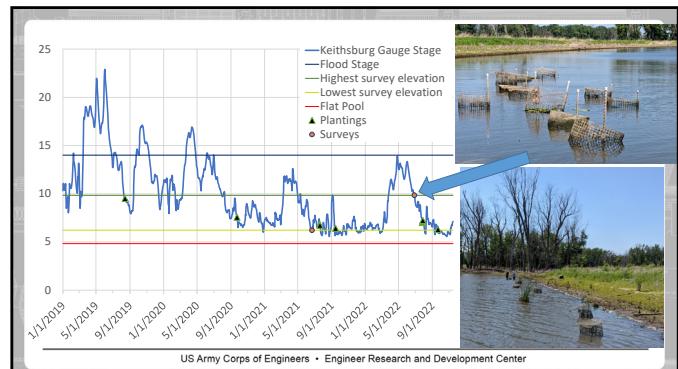

7

8

## FY22 ERDC support:



July 2022



September - 8 weeks later

US Army Corps of Engineers • Engineer Research and Development Center



9


10

## FY22 ERDC support:

- Limited spread observed for both emergents and SAV beyond protected exclosures, likely due to herbivory pressure both aquatic and from terrestrial herbivores
  - Seeds and other propagules produced in protected exclosures for recruitment elsewhere
  - SOW outlines continued monitoring/AM (2-year) - protective exclosures (pens)



US Army Corps of Engineers • Engineer Research and Development Center

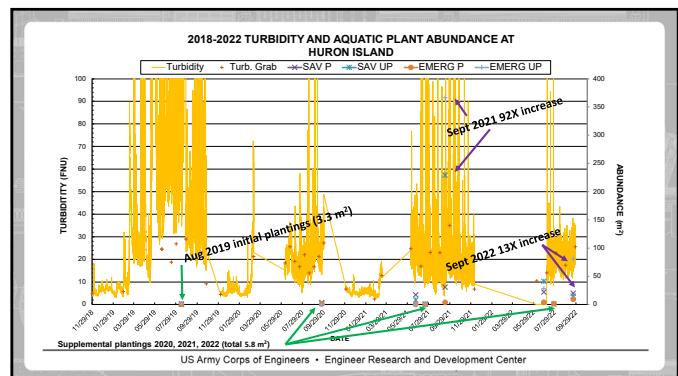

11

12



13
